



SJECCD Measure X Bond Program Master Schedule
Status as of July 1, 2026

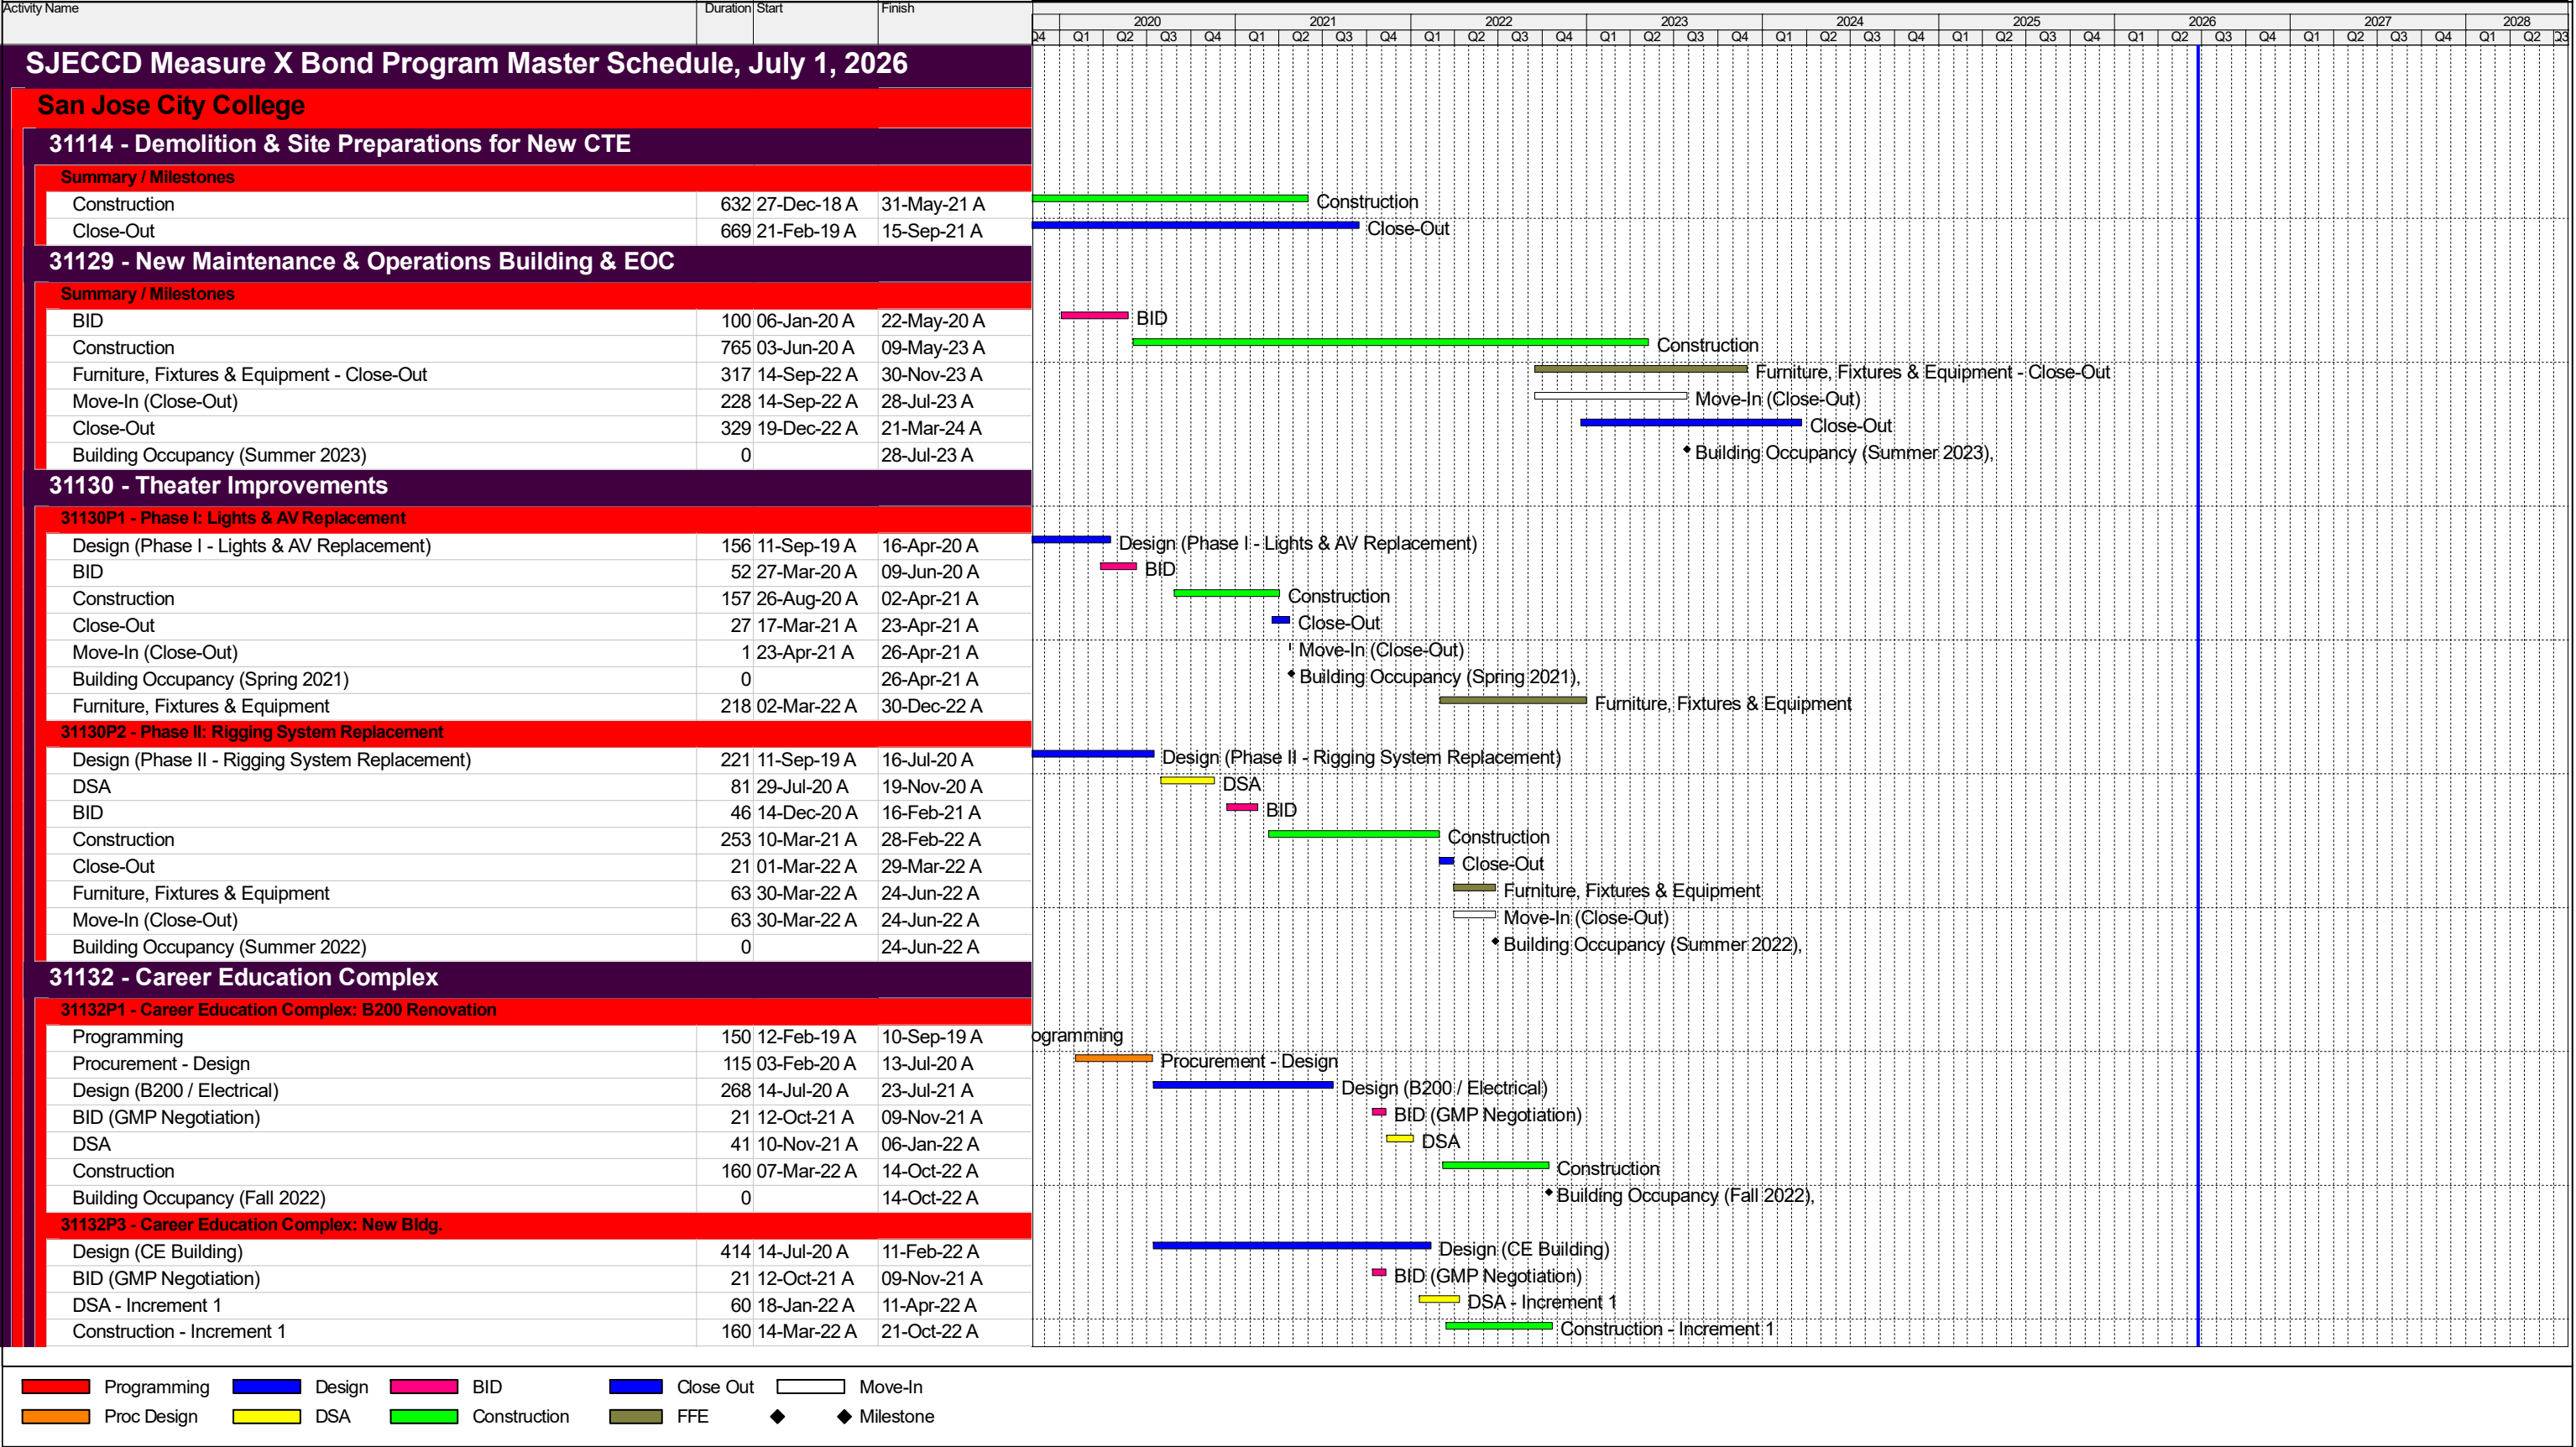

SJECCD Measure X Bond Program Master Schedule
Status as of July 1, 2026

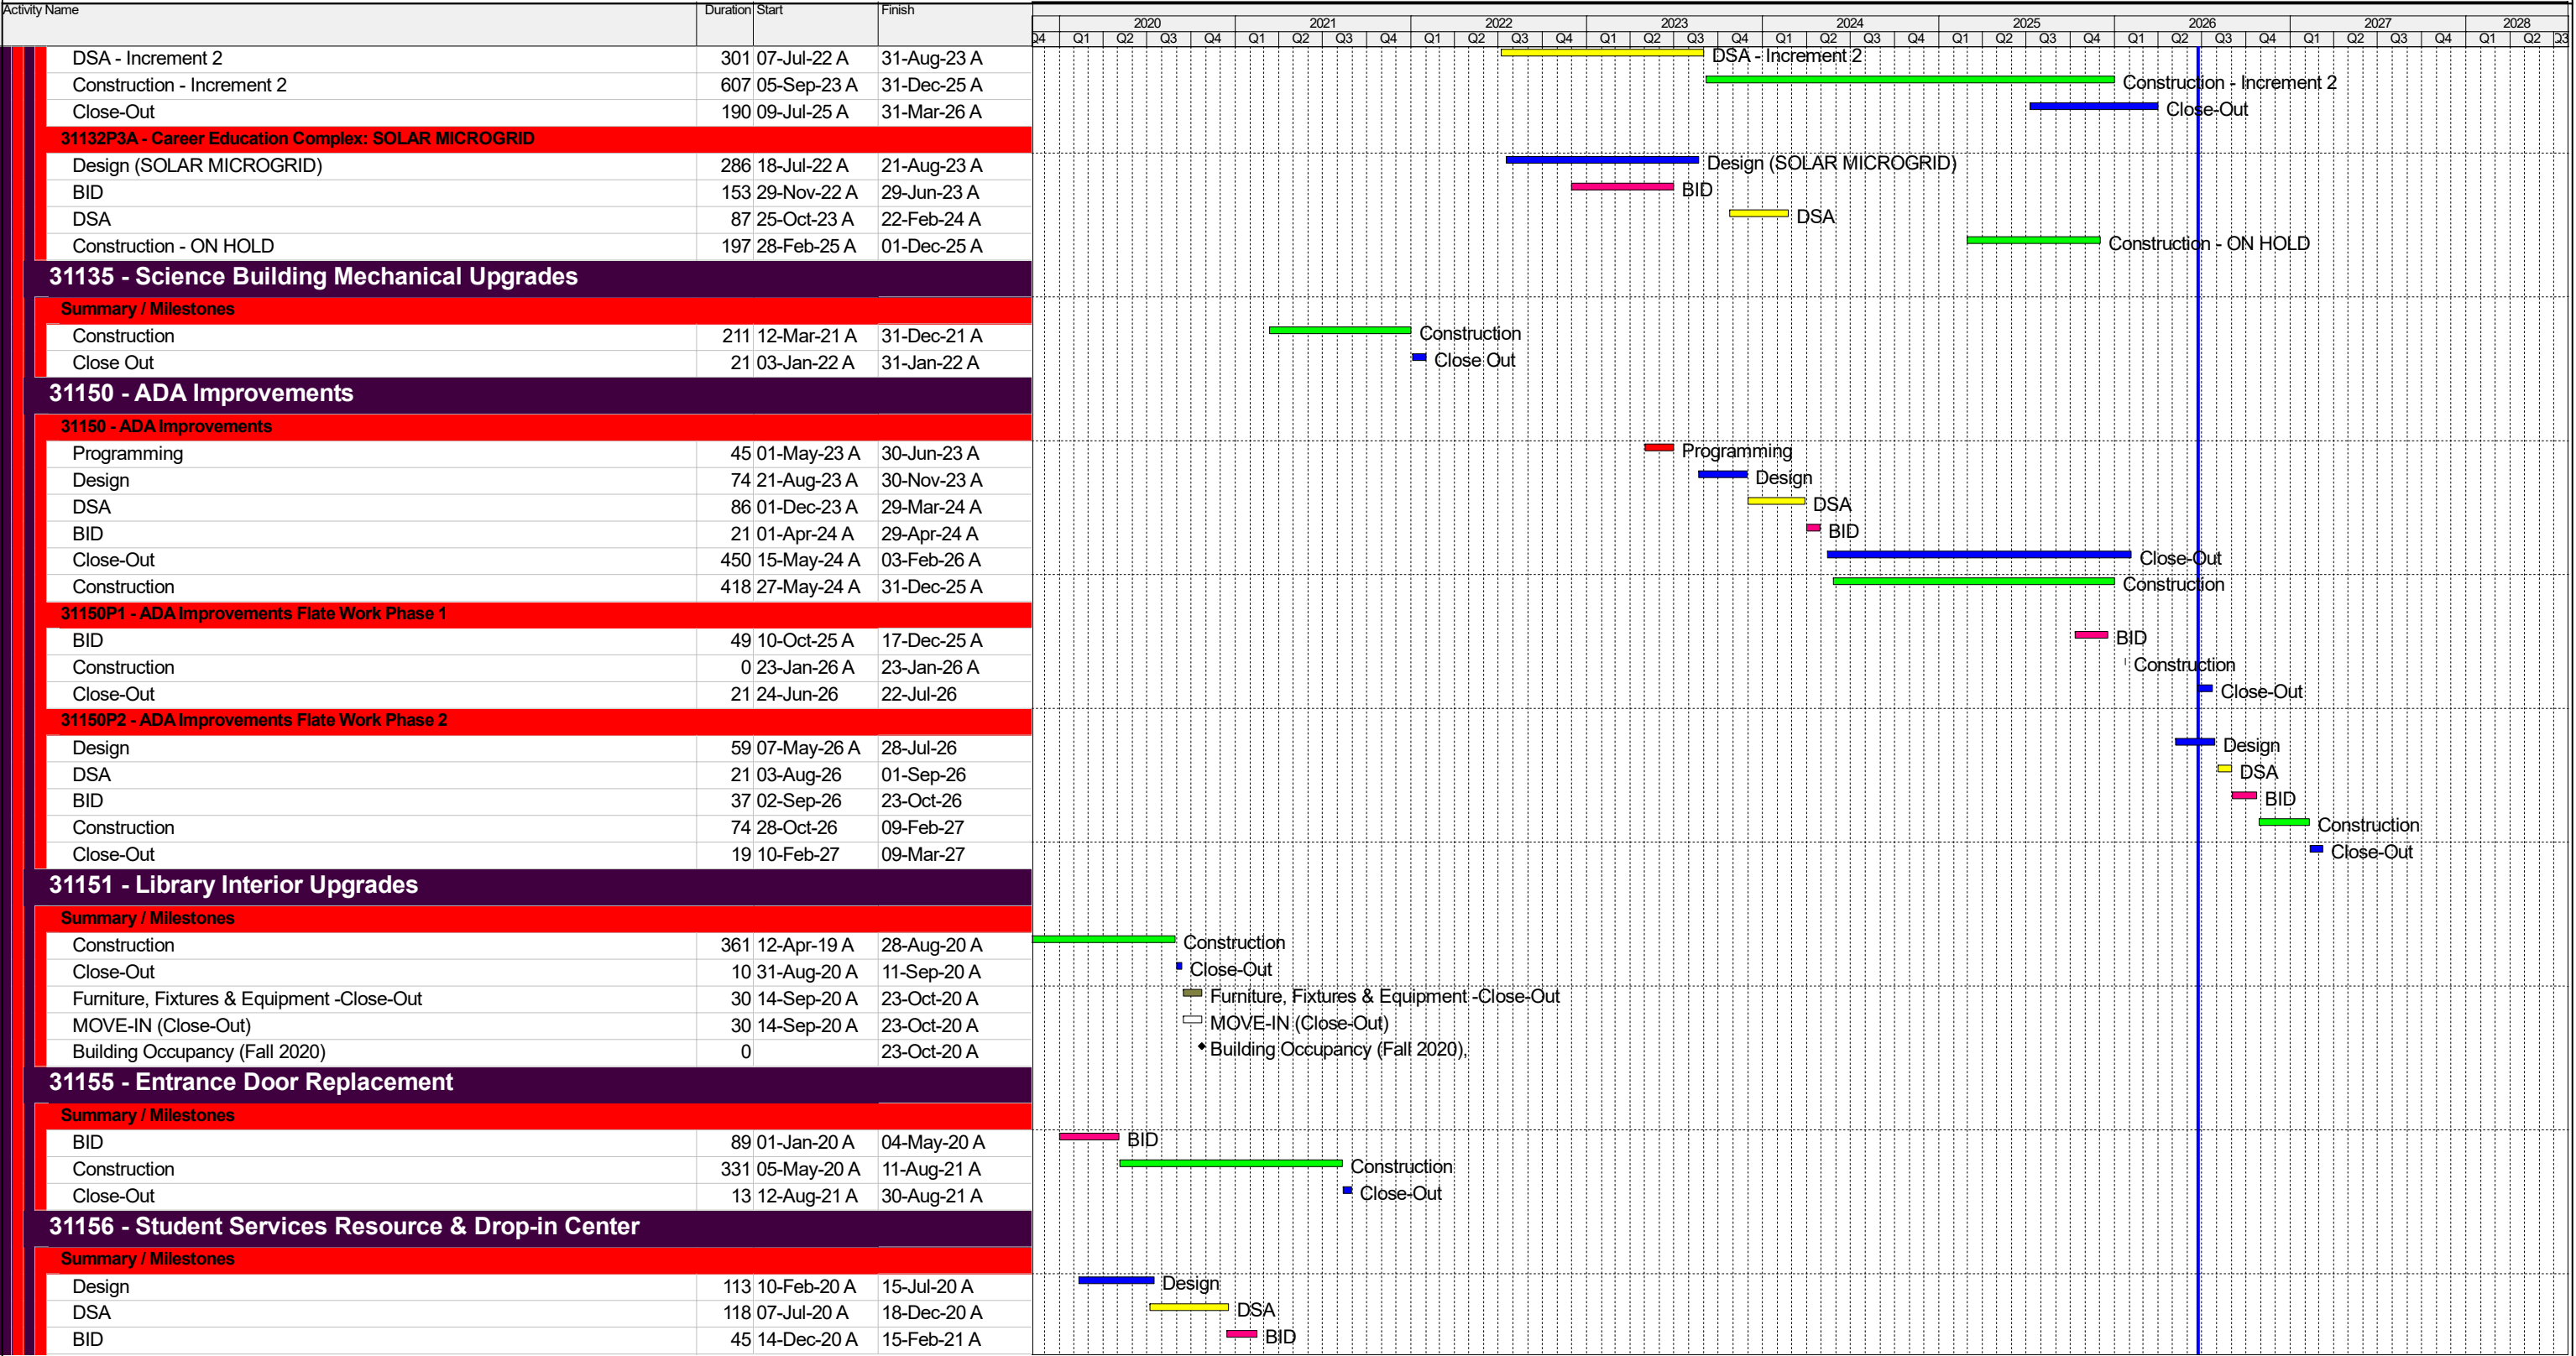


SJECCD Measure X Bond Program Master Schedule
Status as of July 1, 2026

Activity Name	Duration	Start	Finish	Timeline																															
Construction	88	10-Mar-21 A	12-Jul-21 A																																
Close-Out	36	13-Jul-21 A	31-Aug-21 A																																
Furniture, Fixtures & Equipment - Close-Out	44	15-Jul-21 A	15-Sep-21 A																																
Move-In (Close-Out)	44	15-Jul-21 A	15-Sep-21 A																																
Building Occupancy (Summer 2021)	0		15-Sep-21 A																																
31160 - Telecom Master Plan (Master Utility Plan)																																			
Summary / Milestones																																			
Procurement - Design	55	27-Jan-20 A	10-Apr-20 A																																
Design	117	13-Apr-20 A	22-Sep-20 A																																
31163 - Softball Field Renovation																																			
Summary / Milestones																																			
DSA	26	03-Feb-20 A	10-Mar-20 A																																
BID	64	03-Feb-20 A	30-Apr-20 A																																
Construction	88	01-May-20 A	02-Sep-20 A																																
Move-In (Close-Out)	140	26-May-20 A	07-Dec-20 A																																
Close-Out	42	25-Sep-20 A	23-Nov-20 A																																
Building Occupancy (Fall 2020)	0		07-Dec-20 A																																
31164 - Campus HVAC Phase II																																			
Summary / Milestones																																			
Close-Out	41	03-Feb-20 A	30-Mar-20 A																																
31165 - Jaguar Multicultural Center																																			
Summary / Milestones																																			
Programming	123	30-Apr-21 A	19-Oct-21 A																																
31166 - Stadium Renovation																																			
Summary / Milestones																																			
Programming	51	01-Jun-20 A	10-Aug-20 A																																
Design	154	04-Dec-20 A	07-Jul-21 A																																
DSA	78	08-Jul-21 A	25-Oct-21 A																																
BID	26	27-Oct-21 A	01-Dec-21 A																																
Construction	375	28-Jan-22 A	06-Jul-23 A																																
Close-Out	400	19-Sep-22 A	29-Mar-24 A																																
Furniture, Fixtures & Equipment - Close-Out	215	23-Jan-23 A	17-Nov-23 A																																
31167 - Central Plant Rehabilitation																																			
Summary / Milestones																																			
Programming	182	03-Feb-20 A	13-Oct-20 A																																
Design	112	12-Mar-21 A	16-Aug-21 A																																
DSA	130	21-Sep-21 A	21-Mar-22 A																																
BID	44	22-Mar-22 A	20-May-22 A																																
Construction	221	03-Jun-22 A	07-Apr-23 A																																
Close-Out	180	13-Feb-23 A	20-Oct-23 A																																
31169 - CEQA Assessment - SJCC																																			
Summary / Milestones																																			
Procurement - Design	78	21-Feb-20 A	10-Jun-20 A																																
Design	329	11-Jun-20 A	14-Sep-21 A																																
31170 - Elevator Modernization																																			
Summary / Milestones																																			



SJECCD Measure X Bond Program Master Schedule
Status as of July 1, 2026

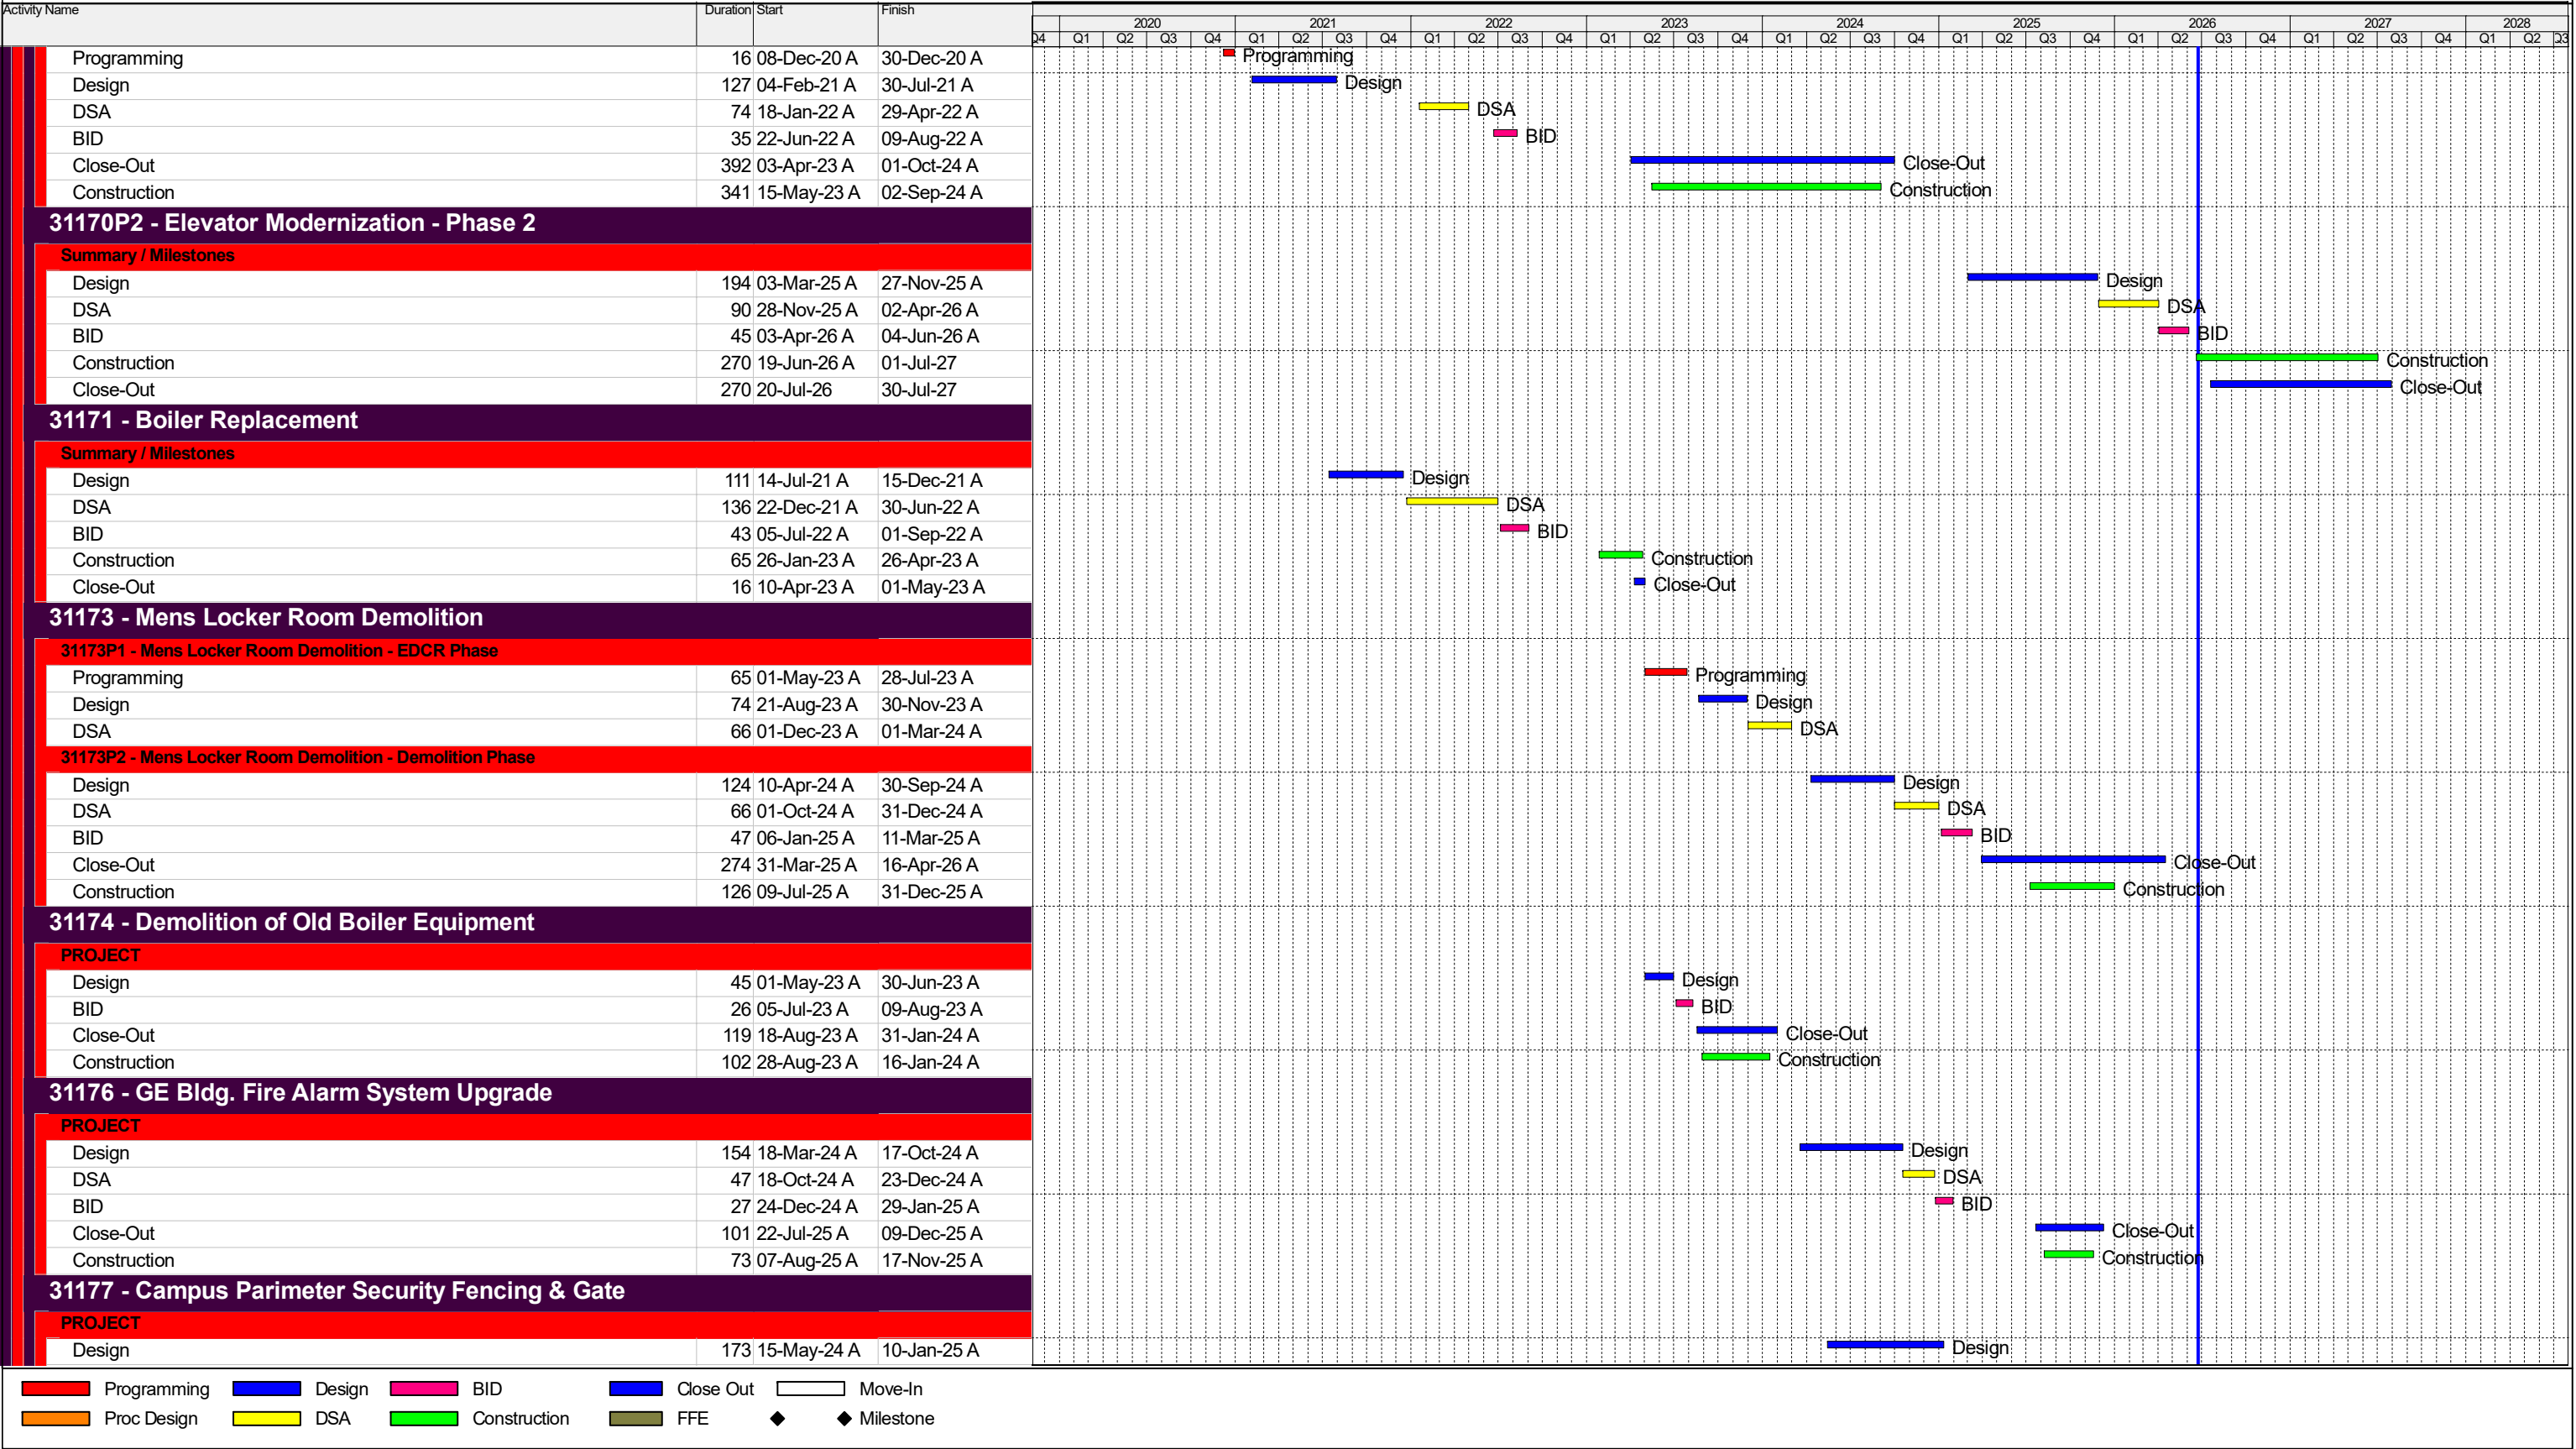

SJECCD Measure X Bond Program Master Schedule
Status as of July 1, 2026


Activity Name				Duration	Start	Finish	Timeline (2020-2028)																															
31178 - Campus Wayfinding & Signage																																						
Summary / Milestones																																						
Procure Design Services				238	03-Feb-25 A	31-Dec-25 A																																
Design				269	18-Feb-25 A	27-Feb-26 A																																
BID				280	04-Aug-25 A	28-Aug-26																																
DSA				130	01-Dec-25 A	29-May-26 A																																
Construction				269	22-Dec-25 A	31-Dec-26																																
Close-Out				280	05-Jan-26 A	29-Jan-27																																
31179 - Sportsfield Scoreboard Replacement																																						
PROJECT																																						
Design				168	26-Feb-24 A	16-Oct-24 A																																
DSA				46	17-Oct-24 A	19-Dec-24 A																																
BID				42	10-Feb-25 A	08-Apr-25 A																																
Construction				94	15-Apr-25 A	22-Aug-25 A																																
Close-Out				76	29-Jul-25 A	11-Nov-25 A																																
31310 - Access Control, Intrusion Alarms, and Monitoring Systems																																						
31310P1A - Access Control, Intrusion Alarms, and Monitoring Systems - Phase 1A																																						
Procurement - Design - Phase 1A				24	06-Apr-20 A	08-May-20 A																																
Design				81	08-May-20 A	31-Aug-20 A																																
BID				40	15-Sep-20 A	10-Nov-20 A																																
Construction				149	01-Dec-20 A	25-Jun-21 A																																
Close-Out				46	28-Jun-21 A	31-Aug-21 A																																
31324 - Restroom Fixtures & Plumbing Upgrades																																						
31324A - Restroom Fixtures & Plumbing Upgrades																																						
Design				217	11-Jun-19 A	09-Apr-20 A																																
DSA				121	15-Oct-19 A	01-Apr-20 A																																
BID				54	10-Apr-20 A	24-Jun-20 A																																
Upgrades- Construction				243	25-Jun-20 A	31-May-21 A																																
Close-Out				109	01-Jun-21 A	29-Oct-21 A																																
31324B - Restroom Maintainace Package																																						
Maintenance - Construction				141	17-Sep-20 A	01-Apr-21 A																																
31346 - Electrical Smart Meters - Campus Wide																																						
Summary / Milestones																																						
Programming				45	01-May-23 A	30-Jun-23 A																																
Design				33	01-Jun-26 A	15-Jul-26																																
BID				49	16-Jul-26	22-Sep-26																																
Construction				130	01-Oct-26	31-Mar-27																																
Close-Out				32	01-Apr-27	14-May-27																																
31350 - Irrigation Modernization & Implementation																																						
Summary / Milestones																																						
Programming				33	01-Apr-26 A	15-May-26 A																																
Design				26	10-Jun-26 A	15-Jul-26																																
BID				39	16-Jul-26	08-Sep-26																																

Programming
 Design
 BID
 Close Out
 Move-In

Proc Design
 DSA
 Construction
 FFE

 Milestone


SJECCD Measure X Bond Program Master Schedule
Status as of July 1, 2026

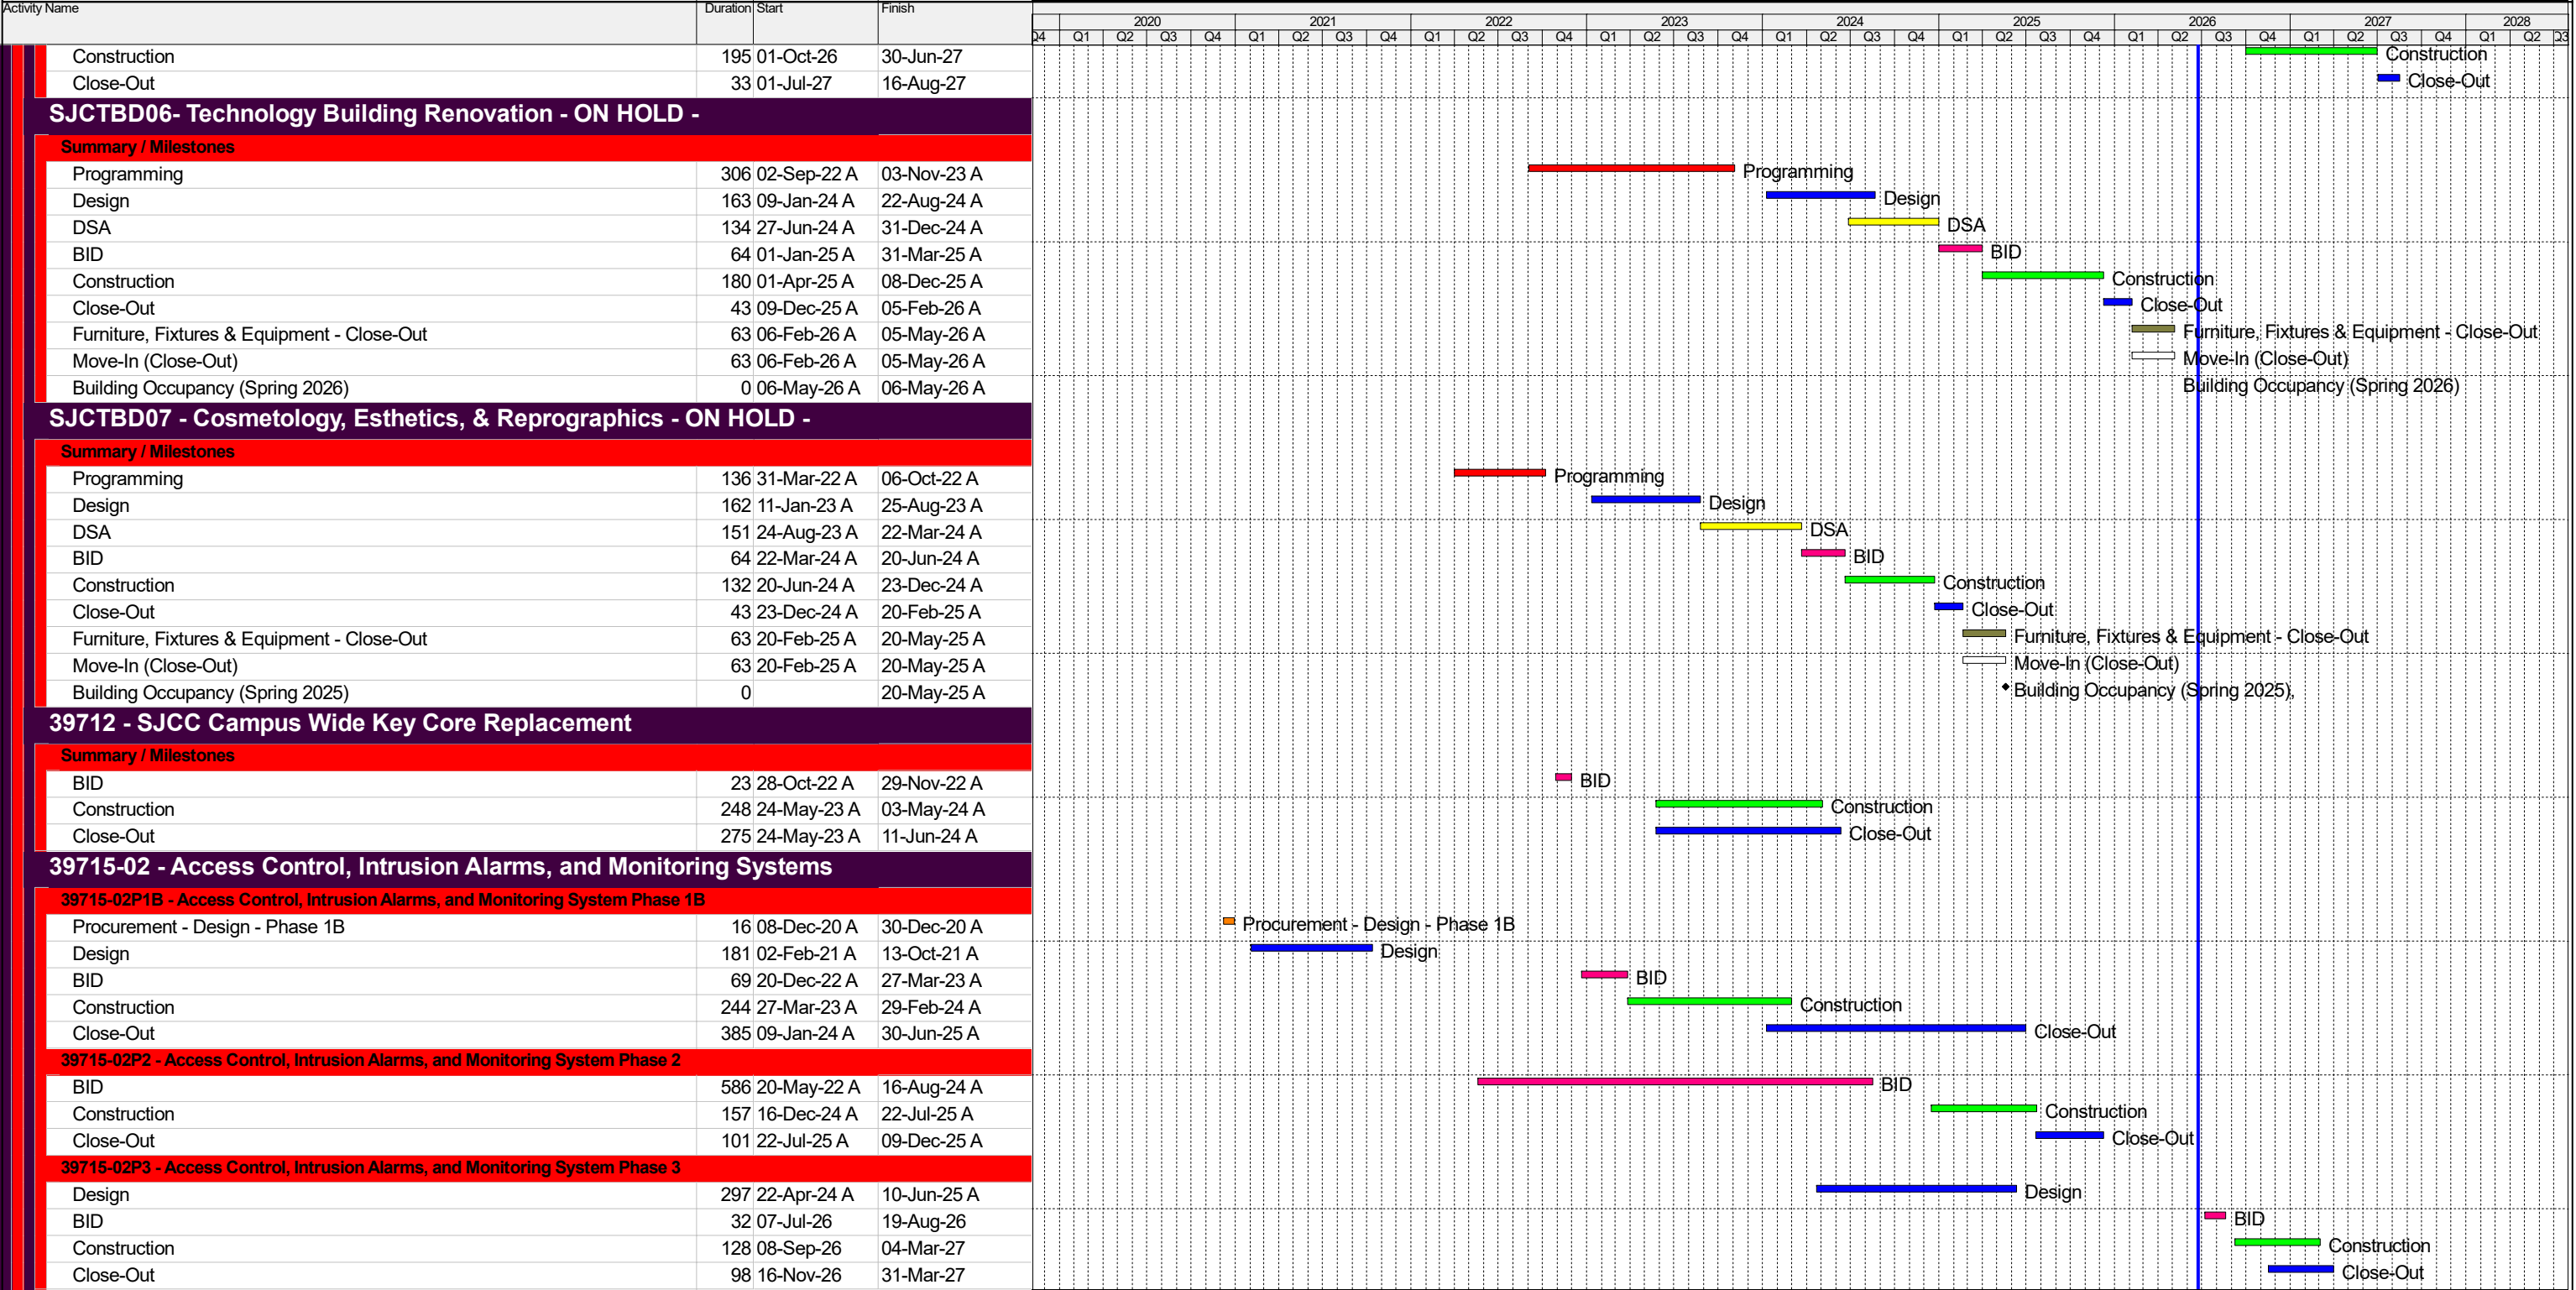

Programming Design BID Close Out Move-In
Proc Design DSA Construction FFE Milestone

SJECCD Measure X Bond Program Master Schedule

Status as of July 1, 2026

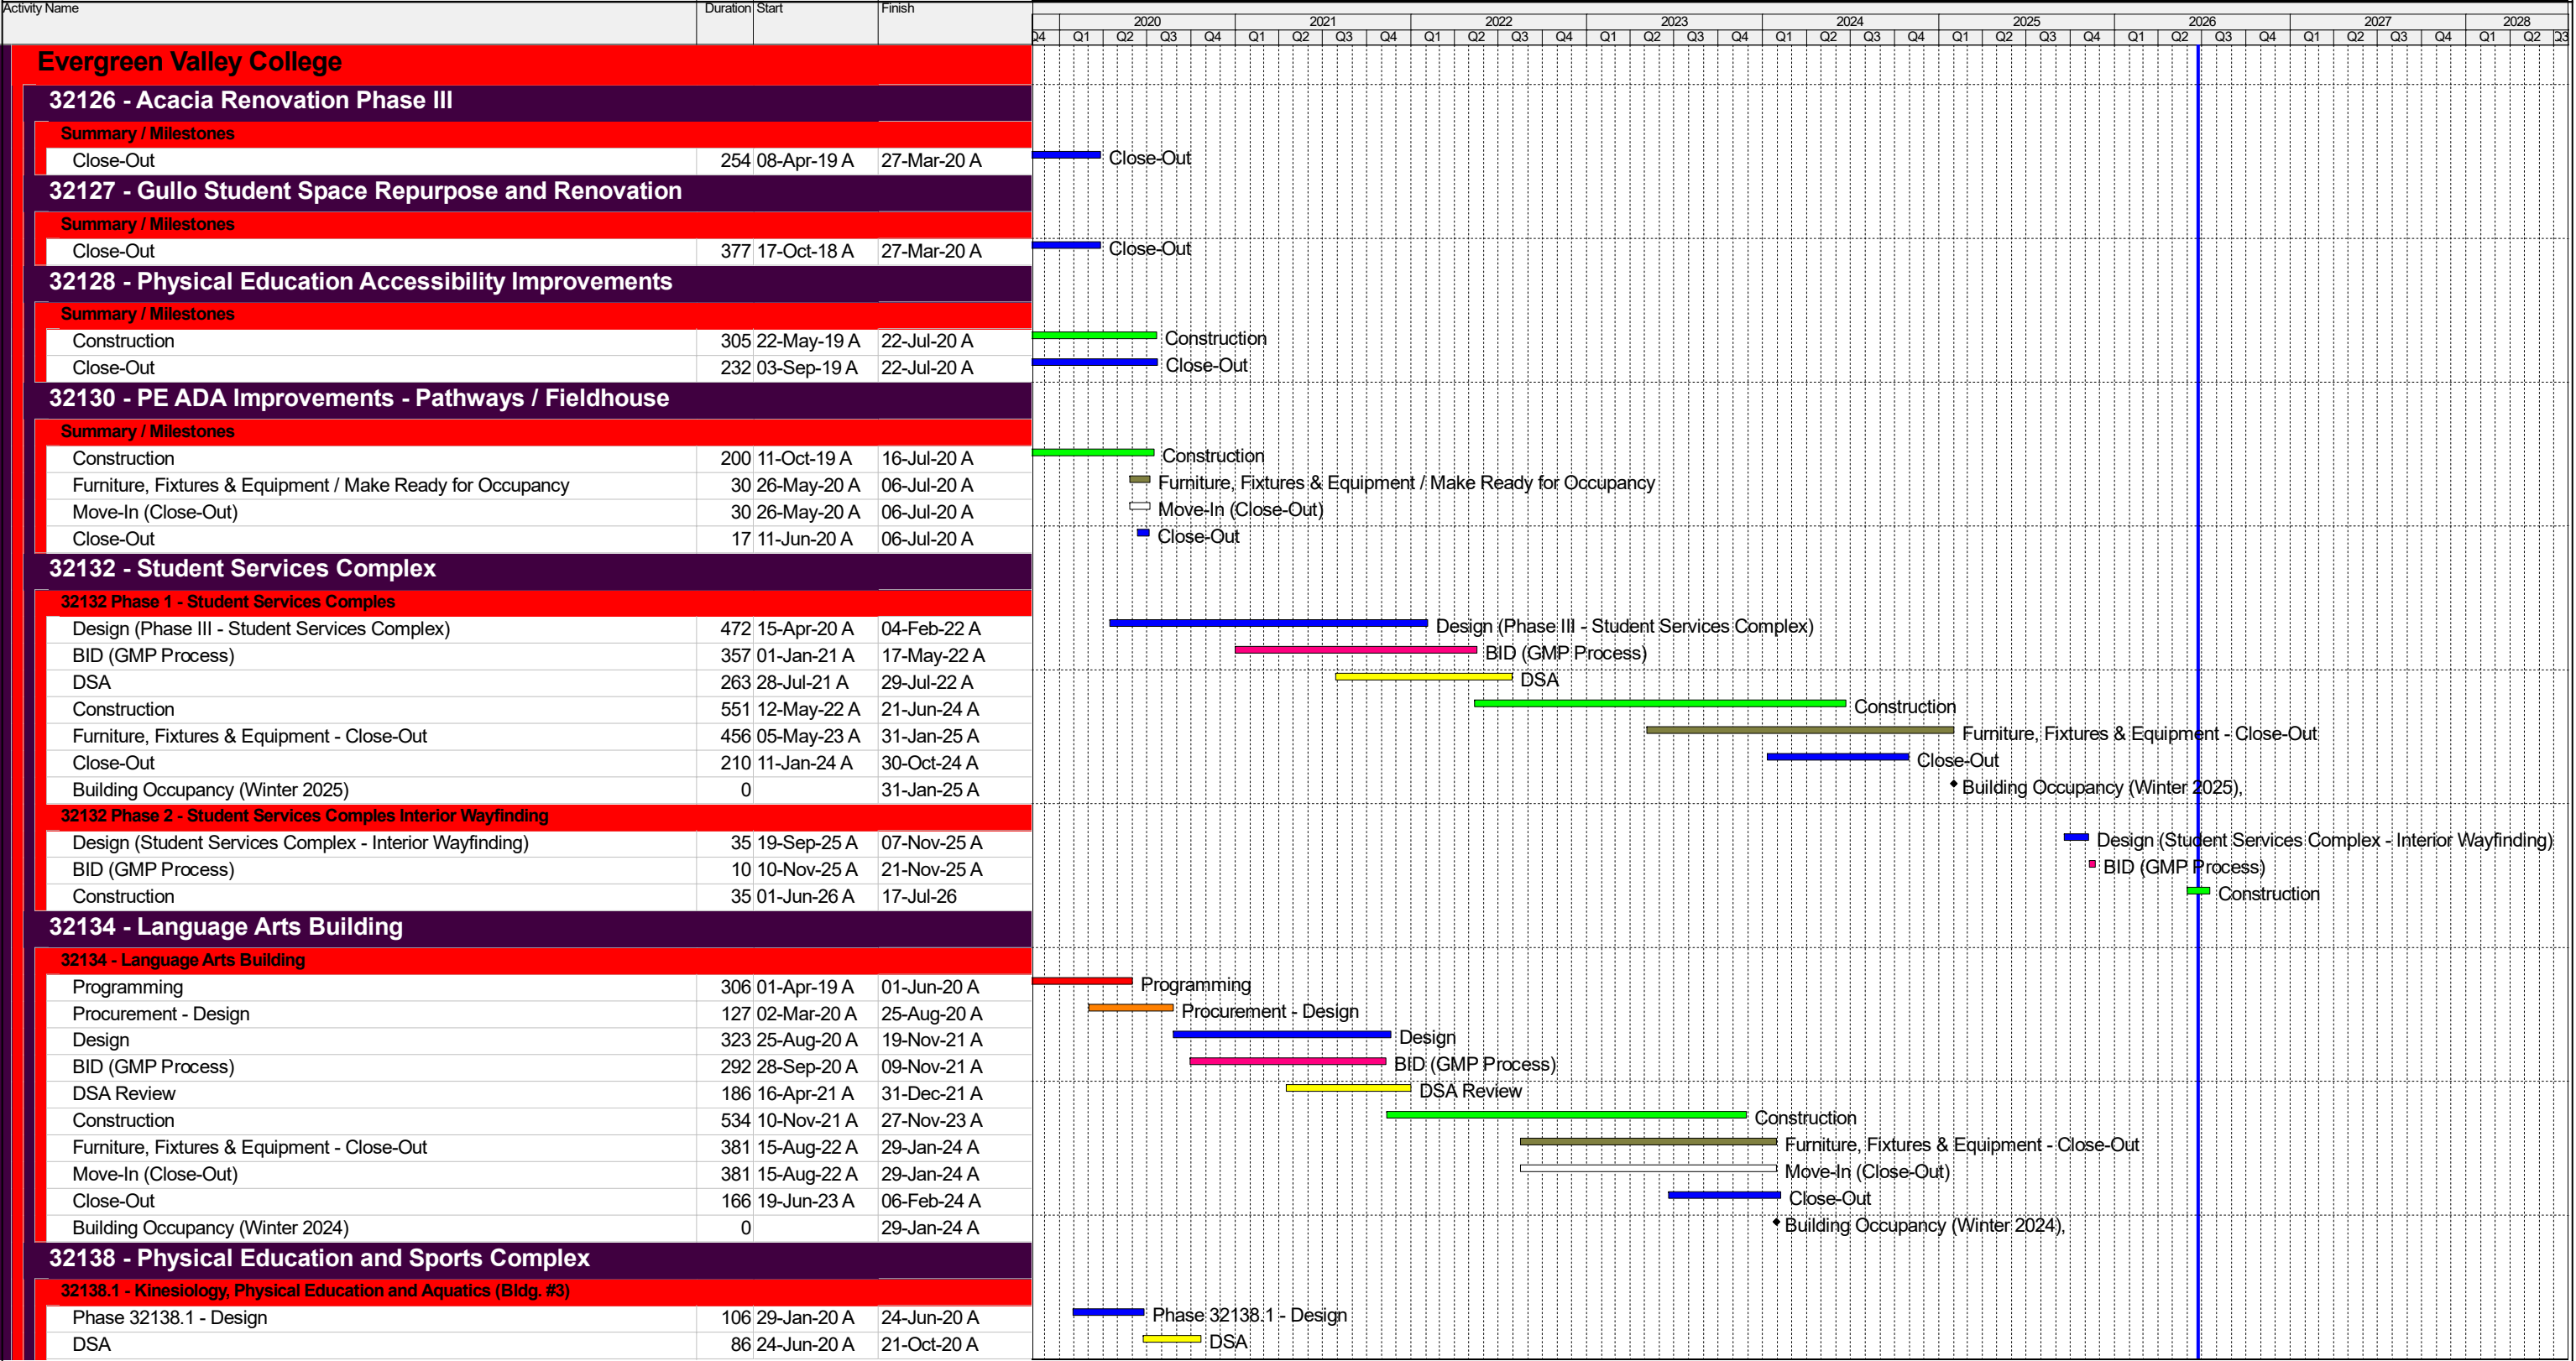

SJECCD Measure X Bond Program Master Schedule Status as of July 1, 2026

Activity Name				Duration	Start	Finish	Timeline																																																																																															
							2020				2021				2022				2023				2024				2025				2026				2027				2028																																																															
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4																																																							
BID				125	24-Jun-20 A	15-Dec-20 A																																										BID																																																						
Construction				182	16-Dec-20 A	27-Aug-21 A																																										Construction																																																						
Furniture, Fixtures & Equipment - Close-Out				193	01-Jun-21 A	25-Feb-22 A																																										Furniture, Fixtures & Equipment - Close-Out																																																						
Move-In (Close-Out)				104	01-Jun-21 A	25-Oct-21 A																																										Move-In (Close-Out)																																																						
Close-Out				11	28-Sep-21 A	12-Oct-21 A																																										Close-Out																																																						
Building Occupancy (Fall 2021)				0		25-Oct-21 A																																										Building Occupancy (Fall 2021)																																																						
32138C - Sports Complex CEQA Analysis																																																																																																						
Phase 32138C - Programming (Sports Complex CEQA Analysis)				48	17-Jul-20 A	22-Sep-20 A																																										Phase: 32138C - Programming (Sports Complex CEQA Analysis)																																																						
32144 - EVC: Campus Painting Project																																																																																																						
32144P3A - Phase 3A EVC: Campus Painting Project																																																																																																						
BID - Phase 3A				70	20-Dec-19 A	27-Mar-20 A																																										BID - Phase 3A																																																						
Construction - Phase 3A				126	17-Mar-20 A	08-Sep-20 A																																										Construction - Phase 3A																																																						
Close-Out - Phase 3A				31	09-Sep-20 A	21-Oct-20 A																																										Close-Out - Phase 3A																																																						
32144P3B - Phase 3B EVC: Campus Painting Project																																																																																																						
BID - Phase 3B				57	06-Mar-20 A	26-May-20 A																																										BID - Phase 3B																																																						
Construction - Phase 3B				174	17-Jun-20 A	15-Feb-21 A																																										Construction - Phase 3B																																																						
Close-Out - Phase 3B				57	25-Jan-21 A	13-Apr-21 A																																										Close-Out - Phase 3B																																																						
32145 - Gullo 2nd Floor - Student Services Center Renovation																																																																																																						
Summary / Milestones																																																																																																						
Close-Out				185	20-Aug-19 A	04-May-20 A																																										Close-Out																																																						
32146 - MS3 Exterior Stair Lighting																																																																																																						
Summary / Milestones																																																																																																						
Close-Out				212	25-Jun-19 A	15-Apr-20 A																																										Close-Out																																																						
32152 - Gullo II Multipurpose Remodel																																																																																																						
Summary / Milestones																																																																																																						
Design				53	01-Nov-19 A	15-Jan-20 A																																										Design																																																						
DSA				97	15-Jan-20 A	29-May-20 A																																										DSA																																																						
BID				38	20-Mar-20 A	13-May-20 A																																										BID																																																						
Construction				228	14-May-20 A	30-Mar-21 A																																										Construction																																																						
Furniture, Fixtures & Equipment- Close-Out				30	19-Oct-20 A	30-Nov-20 A																																										Furniture, Fixtures & Equipment- Close-Out																																																						
Move-In (Close-Out)				30	29-Mar-21 A	10-May-21 A																																										Move-In (Close-Out)																																																						
Close-Out				30	30-Mar-21 A	10-May-21 A																																										Close-Out																																																						
Building Occupancy (Spring 2021)				0		10-May-21 A																																										Building Occupancy (Spring 2021)																																																						
32153 - Sequoia Upgrades / Nursing Addition																																																																																																						
32153 - Sequoia Upgrades / Nursing Addition																																																																																																						
Programming				327	02-Sep-19 A	02-Dec-20 A																																										Programming																																																						
Procurement - Design				88	12-Mar-20 A	14-Jul-20 A																																										Procurement - Design																																																						
Design				417	30-Nov-20 A	05-Jul-22 A																																										Design																																																						
DSA				177	20-Dec-21 A	24-Aug-22 A																																										DSA																																																						
BID				191	21-Dec-21 A	13-Sep-22 A																																										BID																																																						
32153P1 - Sequoia Nursing Addition																																																																																																						
Construction - Nursing Addition				418	14-Oct-22 A	21-May-24 A																																										Construction - Nursing Addition																																																						
Furniture, Fixtures & Equipment - Close-Out				186	13-Oct-23 A	28-Jun-24 A																																										Furniture, Fixtures & Equipment - Close-Out																																																						
Move-In (Close-Out)				138	23-Jan-24 A	01-Aug-24 A																																										Move-In (Close-Out)																																																						
Close-Out				36	22-Mar-24 A	10-May-24 A																																										Close-Out																																																						
Building Occupancy (Summer 2024)				0		01-Aug-24 A																																										Building Occupancy (Summer 2024)																																																						
32153P2 - Sequoia Nursing Rennovation																																																																																																						

Programming

Design

BID

Close Out

Move-In

Proc Design

DSA

Construction

FFE

◆

◆ Milestone

SJECCD Measure X Bond Program Master Schedule
Status as of July 1, 2026

Activity Name			Duration	Start	Finish	Timeline (2020-2028)																															
Construction - Nursing Renovation			136	29-Jul-24 A	03-Feb-25 A	Construction - Nursing Renovation																															
Move-In (Close-Out)			98	30-Oct-24 A	14-Mar-25 A	Move-In (Close-Out)																															
Close-Out			36	17-Jan-25 A	07-Mar-25 A	Close-Out																															
Furniture, Fixtures & Equipment - Close-Out			10	04-Feb-25 A	17-Feb-25 A	Furniture, Fixtures & Equipment - Close-Out																															
Building Occupancy (Winter 2025)			0		14-Mar-25 A	Building Occupancy (Winter 2025),																															
32155 - Cedro Renovation and West Campus ADA Upgrades																																					
Summary / Milestones																																					
Design			160	08-Oct-19 A	19-May-20 A	Design																															
DSA			86	06-Feb-20 A	05-Jun-20 A	DSA																															
BID			54	13-Mar-20 A	28-May-20 A	BID																															
Move-In (Close-Out)			476	21-Aug-20 A	20-Jun-22 A	Move-In (Close-Out)																															
Construction			217	20-Nov-20 A	21-Sep-21 A	Construction																															
Close-Out			419	20-Nov-20 A	29-Jun-22 A	Close-Out																															
Furniture, Fixtures & Equipment - Close-Out			412	20-Nov-20 A	20-Jun-22 A	Furniture, Fixtures & Equipment - Close-Out																															
Building Occupancy (Summer 2022)			0		20-Jun-22 A	Building Occupancy (Summer 2022),																															
32156 - General Education Building																																					
Summary / Milestones																																					
Procurement - Design			88	26-May-20 A	25-Sep-20 A	Procurement - Design																															
Programming			47	08-Sep-20 A	11-Nov-20 A	Programming																															
Design			348	09-Sep-20 A	10-Jan-22 A	Design																															
DSA			247	14-Dec-21 A	23-Nov-22 A	DSA																															
BID			52	02-May-22 A	12-Jul-22 A	BID																															
Construction			487	11-Aug-22 A	21-Jun-24 A	Construction																															
Move-In (Close-Out)			253	22-Jun-23 A	10-Jun-24 A	Move-In (Close-Out)																															
Building Occupancy (Summer 2024)			0		10-Jun-24 A	Building Occupancy (Summer 2024),																															
Close-Out			117	22-Jul-24 A	31-Dec-24 A	Close-Out																															
Furniture, Fixtures & Equipment - Close-Out			36	09-Aug-24 A	30-Sep-24 A	Furniture, Fixtures & Equipment - Close-Out																															
32157 - Student Activities Center - ON HOLD -																																					
Summary / Milestones																																					
Programming			522	03-Jun-19 A	01-Jun-21 A	Programming																															
Procurement - Design			76	01-Sep-21 A	15-Dec-21 A	Procurement - Design																															
Design			359	15-Dec-21 A	01-May-23 A	Design																															
DSA			129	03-May-23 A	30-Oct-23 A	DSA																															
BID			65	31-Oct-23 A	29-Jan-24 A	BID																															
Construction			391	31-Jan-24 A	30-Jul-25 A	Construction																															
Close-Out			65	31-Jul-25 A	29-Oct-25 A	Close-Out																															
Furniture, Fixtures & Equipment - Close-Out			63	31-Jul-25 A	27-Oct-25 A	Furniture, Fixtures & Equipment - Close-Out																															
Move-In (Close-Out)			63	31-Jul-25 A	27-Oct-25 A	Move-In (Close-Out)																															
Building Occupancy (Fall 2025)			0		27-Oct-25 A	Building Occupancy (Fall 2025),																															
32158 - West Campus ADA Upgrades																																					
Summary / Milestones																																					
Design			160	08-Oct-19 A	18-May-20 A	Design																															
BID			158	17-Mar-20 A	22-Oct-20 A	BID																															
DSA			73	19-May-20 A	27-Aug-20 A	DSA																															
Construction			237	23-Oct-20 A	21-Sep-21 A	Construction																															
Close-Out			207	15-Jul-21 A	29-Apr-22 A	Close-Out																															
Close-Out Complete			0		29-Apr-22 A	Close-Out Complete,																															



SJECCD Measure X Bond Program Master Schedule
Status as of July 1, 2026

Activity Name	Duration	Start	Finish	Timeline (2020-2028)																															
32159 - Campus Way Finding / Ground Lighting																																			
Summary / Milestones																																			
Design	199	03-Jun-19 A	06-Mar-20 A																																
DSA	243	06-Feb-20 A	11-Jan-21 A																																
BID	65	25-Feb-20 A	26-May-20 A																																
Construction	554	17-Mar-20 A	02-May-22 A																																
Close-Out	364	02-Mar-22 A	24-Jul-23 A																																
32160 - Security Hardware																																			
Summary / Milestones																																			
BID	59	21-Nov-19 A	12-Feb-20 A																																
Construction	95	12-Feb-20 A	24-Jun-20 A																																
Close-Out	66	31-Mar-20 A	01-Jul-20 A																																
32161 - North Fire Lane / ADA																																			
Summary / Milestones																																			
Design	294	01-Nov-19 A	17-Dec-20 A																																
DSA	98	17-Jul-20 A	01-Dec-20 A																																
BID	132	31-Jul-20 A	01-Feb-21 A																																
Construction	560	09-Feb-21 A	03-Apr-23 A																																
Furniture, Fixtures & Equipment / Make Ready for Occupancy	250	15-Feb-21 A	31-Jan-22 A																																
Close-Out	86	17-Jan-23 A	16-May-23 A																																
32163 - Campus-Wide Building Signage																																			
PROJECT																																			
Procurement - Design	51	03-Feb-20 A	14-Apr-20 A																																
Design	93	15-Apr-20 A	21-Aug-20 A																																
BID	82	24-Aug-20 A	16-Dec-20 A																																
Construction	148	17-Dec-20 A	13-Jul-21 A																																
Close-Out	22	01-Sep-21 A	30-Sep-21 A																																
32164 - EVC CEQA Compliance Consulting Service																																			
Summary / Milestones																																			
Procurement - Design	78	21-Feb-20 A	10-Jun-20 A																																
Design	422	27-Mar-20 A	09-Nov-21 A																																
Administrative Draft EIR	55	19-Apr-21 A	05-Jul-21 A																																
Administrative Final EIR	16	27-Sep-21 A	19-Oct-21 A																																
32165 - MS3 Canopy																																			
32165 - MS3 Canopy																																			
Design	169	13-Mar-20 A	05-Nov-20 A																																
DSA	140	28-Jul-20 A	08-Feb-21 A																																
BID	111	09-Feb-21 A	14-Jul-21 A																																
Construction	173	14-Jul-21 A	15-Mar-22 A																																
Close-Out	32	03-Oct-22 A	15-Nov-22 A																																
32166 - SSC Entry Road and Parking Lot																																			
Summary / Milestones																																			
Design (Phase I - Entry Road and Parking Lot)	596	20-Jan-20 A	02-May-22 A																																
DSA	100	24-Mar-21 A	11-Aug-21 A																																
BID	158	07-Apr-21 A	13-Nov-21 A																																
Construction	543	01-Dec-21 A	29-Dec-23 A																																

Programming
 Design
 BID
 Close Out
 Move-In

Proc Design
 DSA
 Construction
 FFE


 Milestone

SJECCD Measure X Bond Program Master Schedule Status as of July 1, 2026

Activity Name	Duration	Start	Finish	Timeline (2020-2028)																															
Close-Out	109	01-Aug-23 A	29-Dec-23 A																																
32168 - Campus-Wide Signage																																			
32168P1P1 - Design Pkg 1 - Site Signage - Phase 1																																			
Procurement - Design	64	01-Sep-21 A	30-Nov-21 A																																
Design	64	01-Dec-21 A	28-Feb-22 A																																
BID	43	01-Mar-22 A	29-Apr-22 A																																
Construction	64	02-May-22 A	29-Jul-22 A																																
Close-Out	66	01-Aug-22 A	31-Oct-22 A																																
32168P2P1 - Design Pkg 2 - Building Signage - Phase 1																																			
Procurement - Design	64	01-Sep-21 A	30-Nov-21 A																																
Design	86	01-Apr-22 A	29-Jul-22 A																																
BID	44	01-Dec-22 A	31-Jan-23 A																																
Construction	129	01-Feb-23 A	31-Jul-23 A																																
Close-Out	66	01-Aug-23 A	31-Oct-23 A																																
32168P3P2 - Design Pkg 3 - Building Signage - Phase 2																																			
Procurement - Design	65	01-Sep-21 A	30-Nov-21 A																																
Design	172	01-Sep-22 A	28-Apr-23 A																																
BID	66	01-Aug-23 A	31-Oct-23 A																																
Construction	263	17-Nov-23 A	19-Nov-24 A																																
Close-Out	44	23-Sep-24 A	21-Nov-24 A																																
32168P3P3 - Design Pkg 3 - Site Signage - Phase 3																																			
Procurement - Design	64	01-Sep-21 A	30-Nov-21 A																																
Design	432	01-Sep-22 A	29-Apr-24 A																																
BID	66	01-Aug-23 A	31-Oct-23 A																																
Construction	336	17-Nov-23 A	28-Feb-25 A																																
Close-Out	105	09-Oct-24 A	04-Mar-25 A																																
32317 - Pavement Preservation / Roadway and Curb Marking																																			
Summary / Milestones																																			
Construction	219	17-Jun-19 A	16-Apr-20 A																																
Close-Out	10	03-Apr-20 A	16-Apr-20 A																																
32327 - Electrical Smart Meters Campus Wide																																			
Summary / Milestones																																			
Programming	45	01-May-23 A	30-Jun-23 A																																
Design	33	01-Jun-26 A	15-Jul-26																																
BID	49	16-Jul-26	22-Sep-26																																
Construction	130	01-Oct-26	31-Mar-27																																
Close-Out	32	01-Apr-27	14-May-27																																
EVCTBD07 Environmental Controls Update																																			
Summary / Milestones																																			
Procurement - Design	52	02-Nov-20 A	12-Jan-21 A																																
Construction	135	24-Dec-21 A	30-Jun-22 A																																
Close-Out	160	22-Jun-22 A	31-Jan-23 A																																



SJECCD Measure X Bond Program Master Schedule
Status as of July 1, 2026

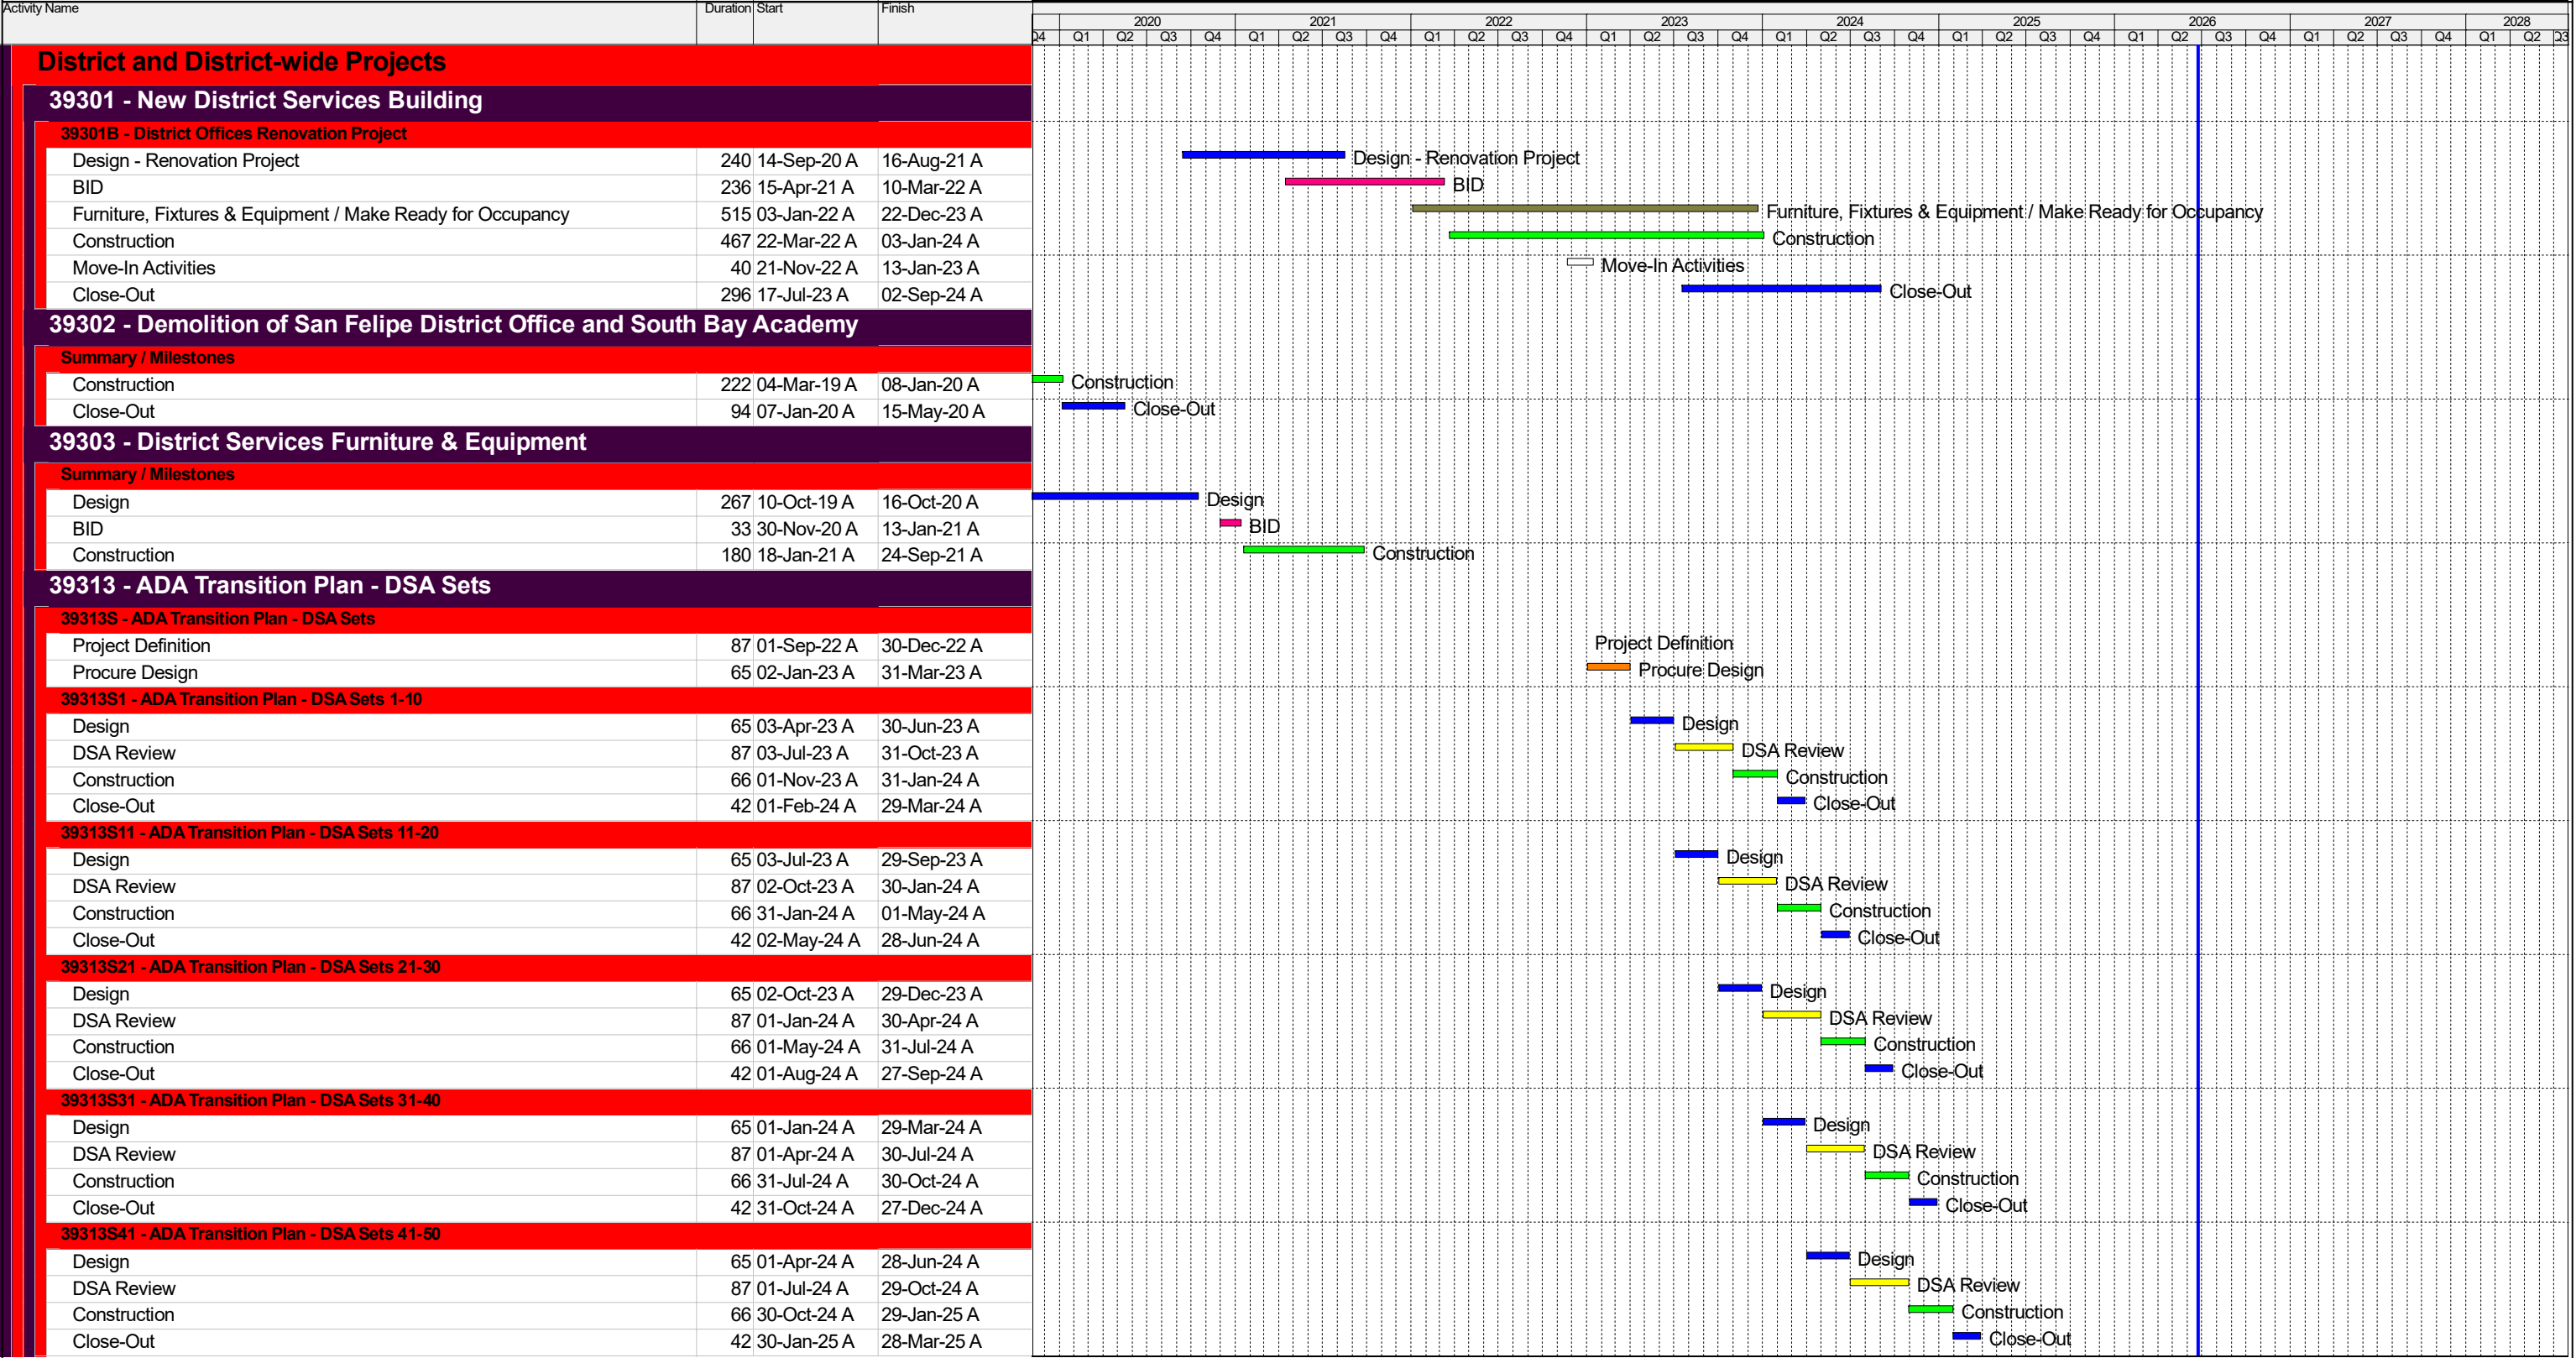

SJECCD Measure X Bond Program Master Schedule
Status as of July 1, 2026

Activity Name	Duration	Start	Finish	Timeline (2020-2028)																															
39314 - District Office Elevators Safety and Accessibility Upgrades																																			
Summary / Milestones																																			
Design	59	02-Dec-19 A	21-Feb-20 A																																
BID	83	17-Feb-20 A	10-Jun-20 A																																
Construction	283	02-Jun-20 A	01-Jul-21 A																																
Close-Out	31	02-Jul-21 A	13-Aug-21 A																																
39315 - District Elevator Assessment																																			
Summary / Milestones																																			
Procurement - Design	55	26-Nov-19 A	11-Feb-20 A																																
Design	128	12-Feb-20 A	07-Aug-20 A																																
39629 - District Warehouse & Operations Facility																																			
39629P1 - District Wearhouse & Operations Facility - Phase 1																																			
Project Definition	64	02-May-22 A	29-Jul-22 A																																
Procure Design	132	01-Aug-22 A	31-Jan-23 A																																
Programming	63	01-Feb-23 A	28-Apr-23 A																																
Design	219	01-May-23 A	29-Feb-24 A																																
DSA Review	86	01-Mar-24 A	28-Jun-24 A																																
Construction - New Addition & Site	196	01-Jul-24 A	31-Mar-25 A																																
Close-Out	65	01-Apr-25 A	30-Jun-25 A																																
39629P2 - District Wearhouse & Operations Facility - Phase 2																																			
Construction - Renovation	195	02-Jun-25 A	27-Feb-26 A																																
Close-Out	65	02-Mar-26 A	29-May-26 A																																
39632 - District Wide Central Plant Upgrade																																			
Summary / Milestones																																			
Procurement - Design	85	01-Apr-22 A	29-Jul-22 A																																
Design	152	01-Aug-22 A	28-Feb-23 A																																
DSA	260	02-Dec-24 A	28-Nov-25 A																																
Construction	262	13-Jan-26 A	13-Jan-27																																
Close-Out	65	15-Jan-27	15-Apr-27																																

