


SJECCD Measure X Bond Program Master Schedule
Status as of September 1, 2026



SJECCD Measure X Bond Program Master Schedule Status as of September 1, 2026

Activity Name	Duration	Start	Finish	Timeline (2020-2028)																															
31132P3A - Career Education Complex: SOLAR MICROGRID																																			
DSA - Increment 2	301	07-Jul-22 A	31-Aug-23 A	DSA - Increment 2																															
Construction - Increment 2	607	05-Sep-23 A	31-Dec-25 A	Construction - Increment 2																															
Close-Out	190	09-Jul-25 A	31-Mar-26 A	Close-Out																															
31135 - Science Building Mechanical Upgrades																																			
Summary / Milestones																																			
Construction	211	12-Mar-21 A	31-Dec-21 A	Construction																															
Close Out	21	03-Jan-22 A	31-Jan-22 A	Close Out																															
31150 - ADA Improvements																																			
31150 - ADA Improvements																																			
Programming	45	01-May-23 A	30-Jun-23 A	Programming																															
Design	74	21-Aug-23 A	30-Nov-23 A	Design																															
DSA	86	01-Dec-23 A	29-Mar-24 A	DSA																															
BID	21	01-Apr-24 A	29-Apr-24 A	BID																															
Close-Out	450	15-May-24 A	03-Feb-26 A	Close-Out																															
Construction	418	27-May-24 A	31-Dec-25 A	Construction																															
31150P1 - ADA Improvements Flate Work Phase 1																																			
BID	49	10-Oct-25 A	17-Dec-25 A	BID																															
Construction	149	06-Jan-26 A	31-Jul-26 A	Construction																															
Close-Out	21	31-Jul-26 A	31-Aug-26	Close-Out																															
31150P2 - ADA Improvements Flate Work Phase 2																																			
Design	86	07-May-26 A	03-Sep-26	Design																															
DSA	22	08-Sep-26	08-Oct-26	DSA																															
BID	38	08-Oct-26	01-Dec-26	BID																															
Construction	75	03-Dec-26	18-Mar-27	Construction																															
Close-Out	20	18-Mar-27	15-Apr-27	Close-Out																															
31151 - Library Interior Upgrades																																			
Summary / Milestones																																			
Construction	361	12-Apr-19 A	28-Aug-20 A	Construction																															
Close-Out	10	31-Aug-20 A	11-Sep-20 A	Close-Out																															
Furniture, Fixtures & Equipment -Close-Out	30	14-Sep-20 A	23-Oct-20 A	Furniture, Fixtures & Equipment -Close-Out																															
MOVE-IN (Close-Out)	30	14-Sep-20 A	23-Oct-20 A	MOVE-IN (Close-Out)																															
Building Occupancy (Fall 2020)	0		23-Oct-20 A	Building Occupancy (Fall 2020)																															
31155 - Entrance Door Replacement																																			
Summary / Milestones																																			
BID	89	01-Jan-20 A	04-May-20 A	BID																															
Construction	331	05-May-20 A	11-Aug-21 A	Construction																															
Close-Out	13	12-Aug-21 A	30-Aug-21 A	Close-Out																															
31156 - Student Services Resource & Drop-in Center																																			
Summary / Milestones																																			
Design	113	10-Feb-20 A	15-Jul-20 A	Design																															
DSA	118	07-Jul-20 A	18-Dec-20 A	DSA																															
BID	45	14-Dec-20 A	15-Feb-21 A	BID																															

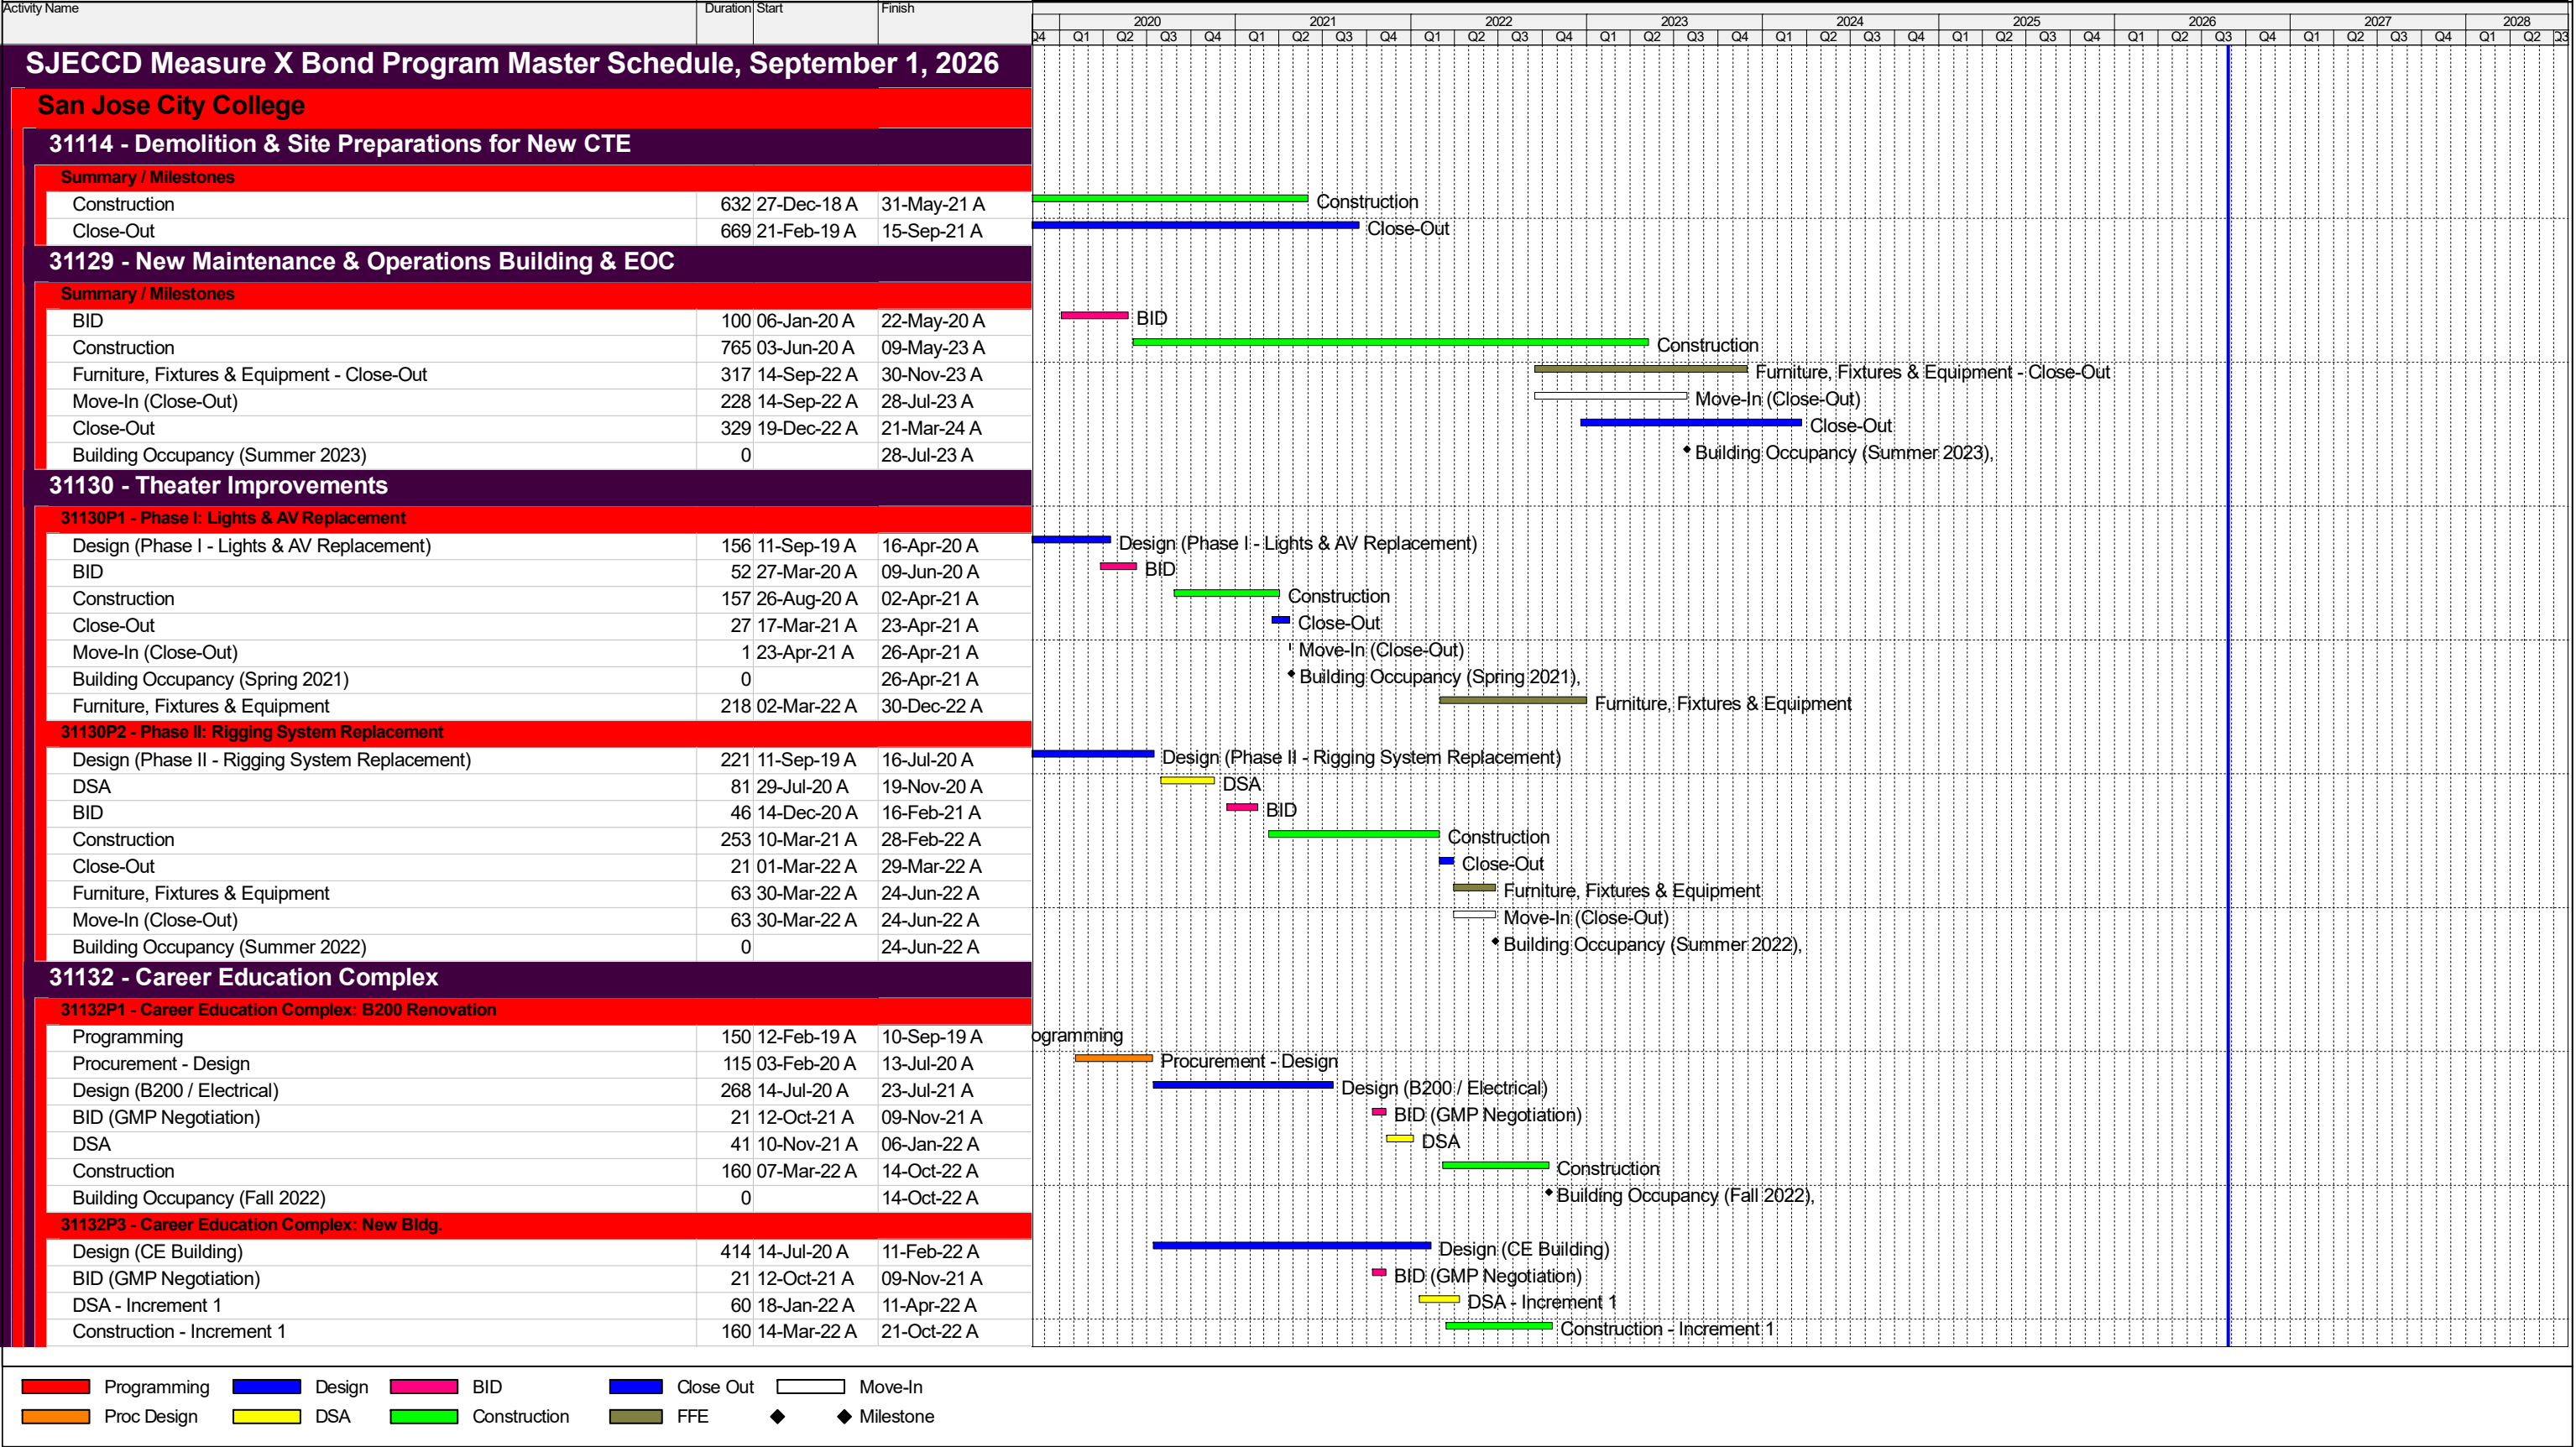


SJECCD Measure X Bond Program Master Schedule
Status as of September 1, 2026


Activity Name	Duration	Start	Finish	Timeline																															
Construction	88	10-Mar-21 A	12-Jul-21 A																																
Close-Out	36	13-Jul-21 A	31-Aug-21 A																																
Furniture, Fixtures & Equipment - Close-Out	44	15-Jul-21 A	15-Sep-21 A																																
Move-In (Close-Out)	44	15-Jul-21 A	15-Sep-21 A																																
Building Occupancy (Summer 2021)	0		15-Sep-21 A																																
31160 - Telecom Master Plan (Master Utility Plan)																																			
Summary / Milestones																																			
Procurement - Design	55	27-Jan-20 A	10-Apr-20 A																																
Design	117	13-Apr-20 A	22-Sep-20 A																																
31163 - Softball Field Renovation																																			
Summary / Milestones																																			
DSA	26	03-Feb-20 A	10-Mar-20 A																																
BID	64	03-Feb-20 A	30-Apr-20 A																																
Construction	88	01-May-20 A	02-Sep-20 A																																
Move-In (Close-Out)	140	26-May-20 A	07-Dec-20 A																																
Close-Out	42	25-Sep-20 A	23-Nov-20 A																																
Building Occupancy (Fall 2020)	0		07-Dec-20 A																																
31164 - Campus HVAC Phase II																																			
Summary / Milestones																																			
Close-Out	41	03-Feb-20 A	30-Mar-20 A																																
31165 - Jaguar Multicultural Center																																			
Summary / Milestones																																			
Programming	123	30-Apr-21 A	19-Oct-21 A																																
31166 - Stadium Renovation																																			
Summary / Milestones																																			
Programming	51	01-Jun-20 A	10-Aug-20 A																																
Design	154	04-Dec-20 A	07-Jul-21 A																																
DSA	78	08-Jul-21 A	25-Oct-21 A																																
BID	26	27-Oct-21 A	01-Dec-21 A																																
Construction	375	28-Jan-22 A	06-Jul-23 A																																
Close-Out	400	19-Sep-22 A	29-Mar-24 A																																
Furniture, Fixtures & Equipment - Close-Out	215	23-Jan-23 A	17-Nov-23 A																																
31167 - Central Plant Rehabilitation																																			
Summary / Milestones																																			
Programming	182	03-Feb-20 A	13-Oct-20 A																																
Design	112	12-Mar-21 A	16-Aug-21 A																																
DSA	130	21-Sep-21 A	21-Mar-22 A																																
BID	44	22-Mar-22 A	20-May-22 A																																
Construction	221	03-Jun-22 A	07-Apr-23 A																																
Close-Out	180	13-Feb-23 A	20-Oct-23 A																																
31169 - CEQA Assessment - SJCC																																			
Summary / Milestones																																			
Procurement - Design	78	21-Feb-20 A	10-Jun-20 A																																
Design	329	11-Jun-20 A	14-Sep-21 A																																
31170 - Elevator Modernization																																			
Summary / Milestones																																			



SJECCD Measure X Bond Program Master Schedule
Status as of September 1, 2026

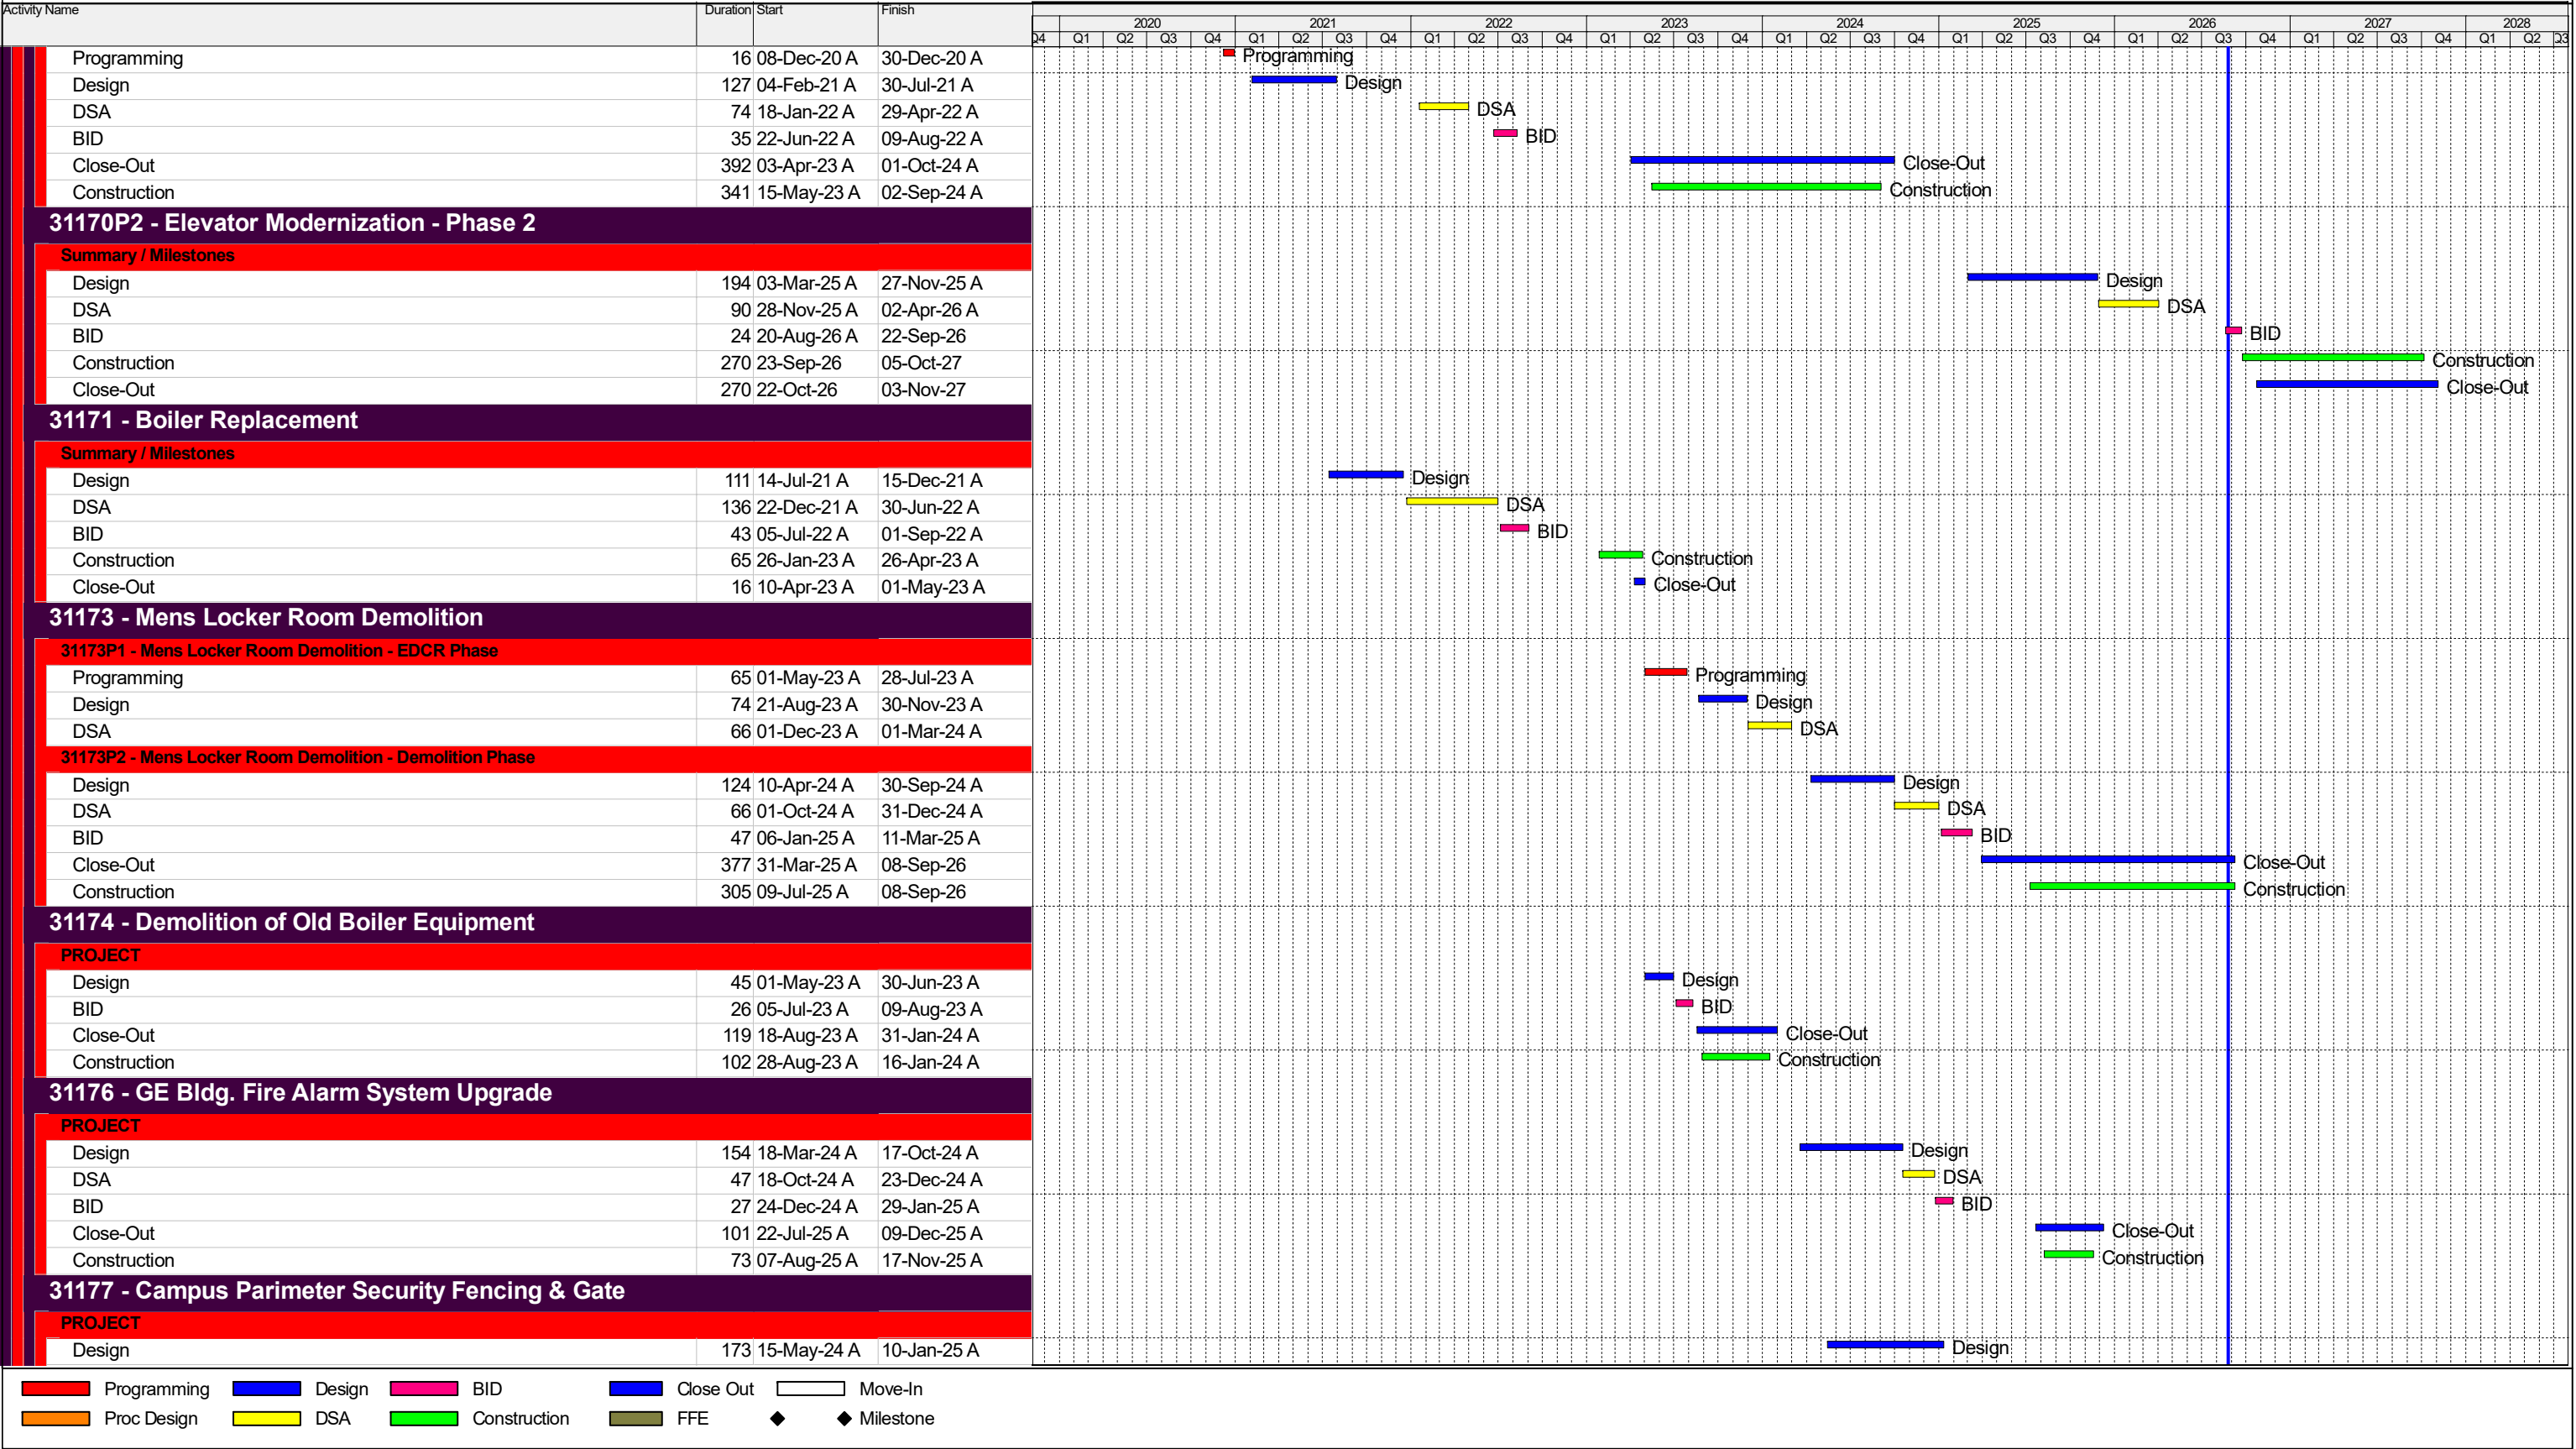

SJECCD Measure X Bond Program Master Schedule
Status as of September 1, 2026

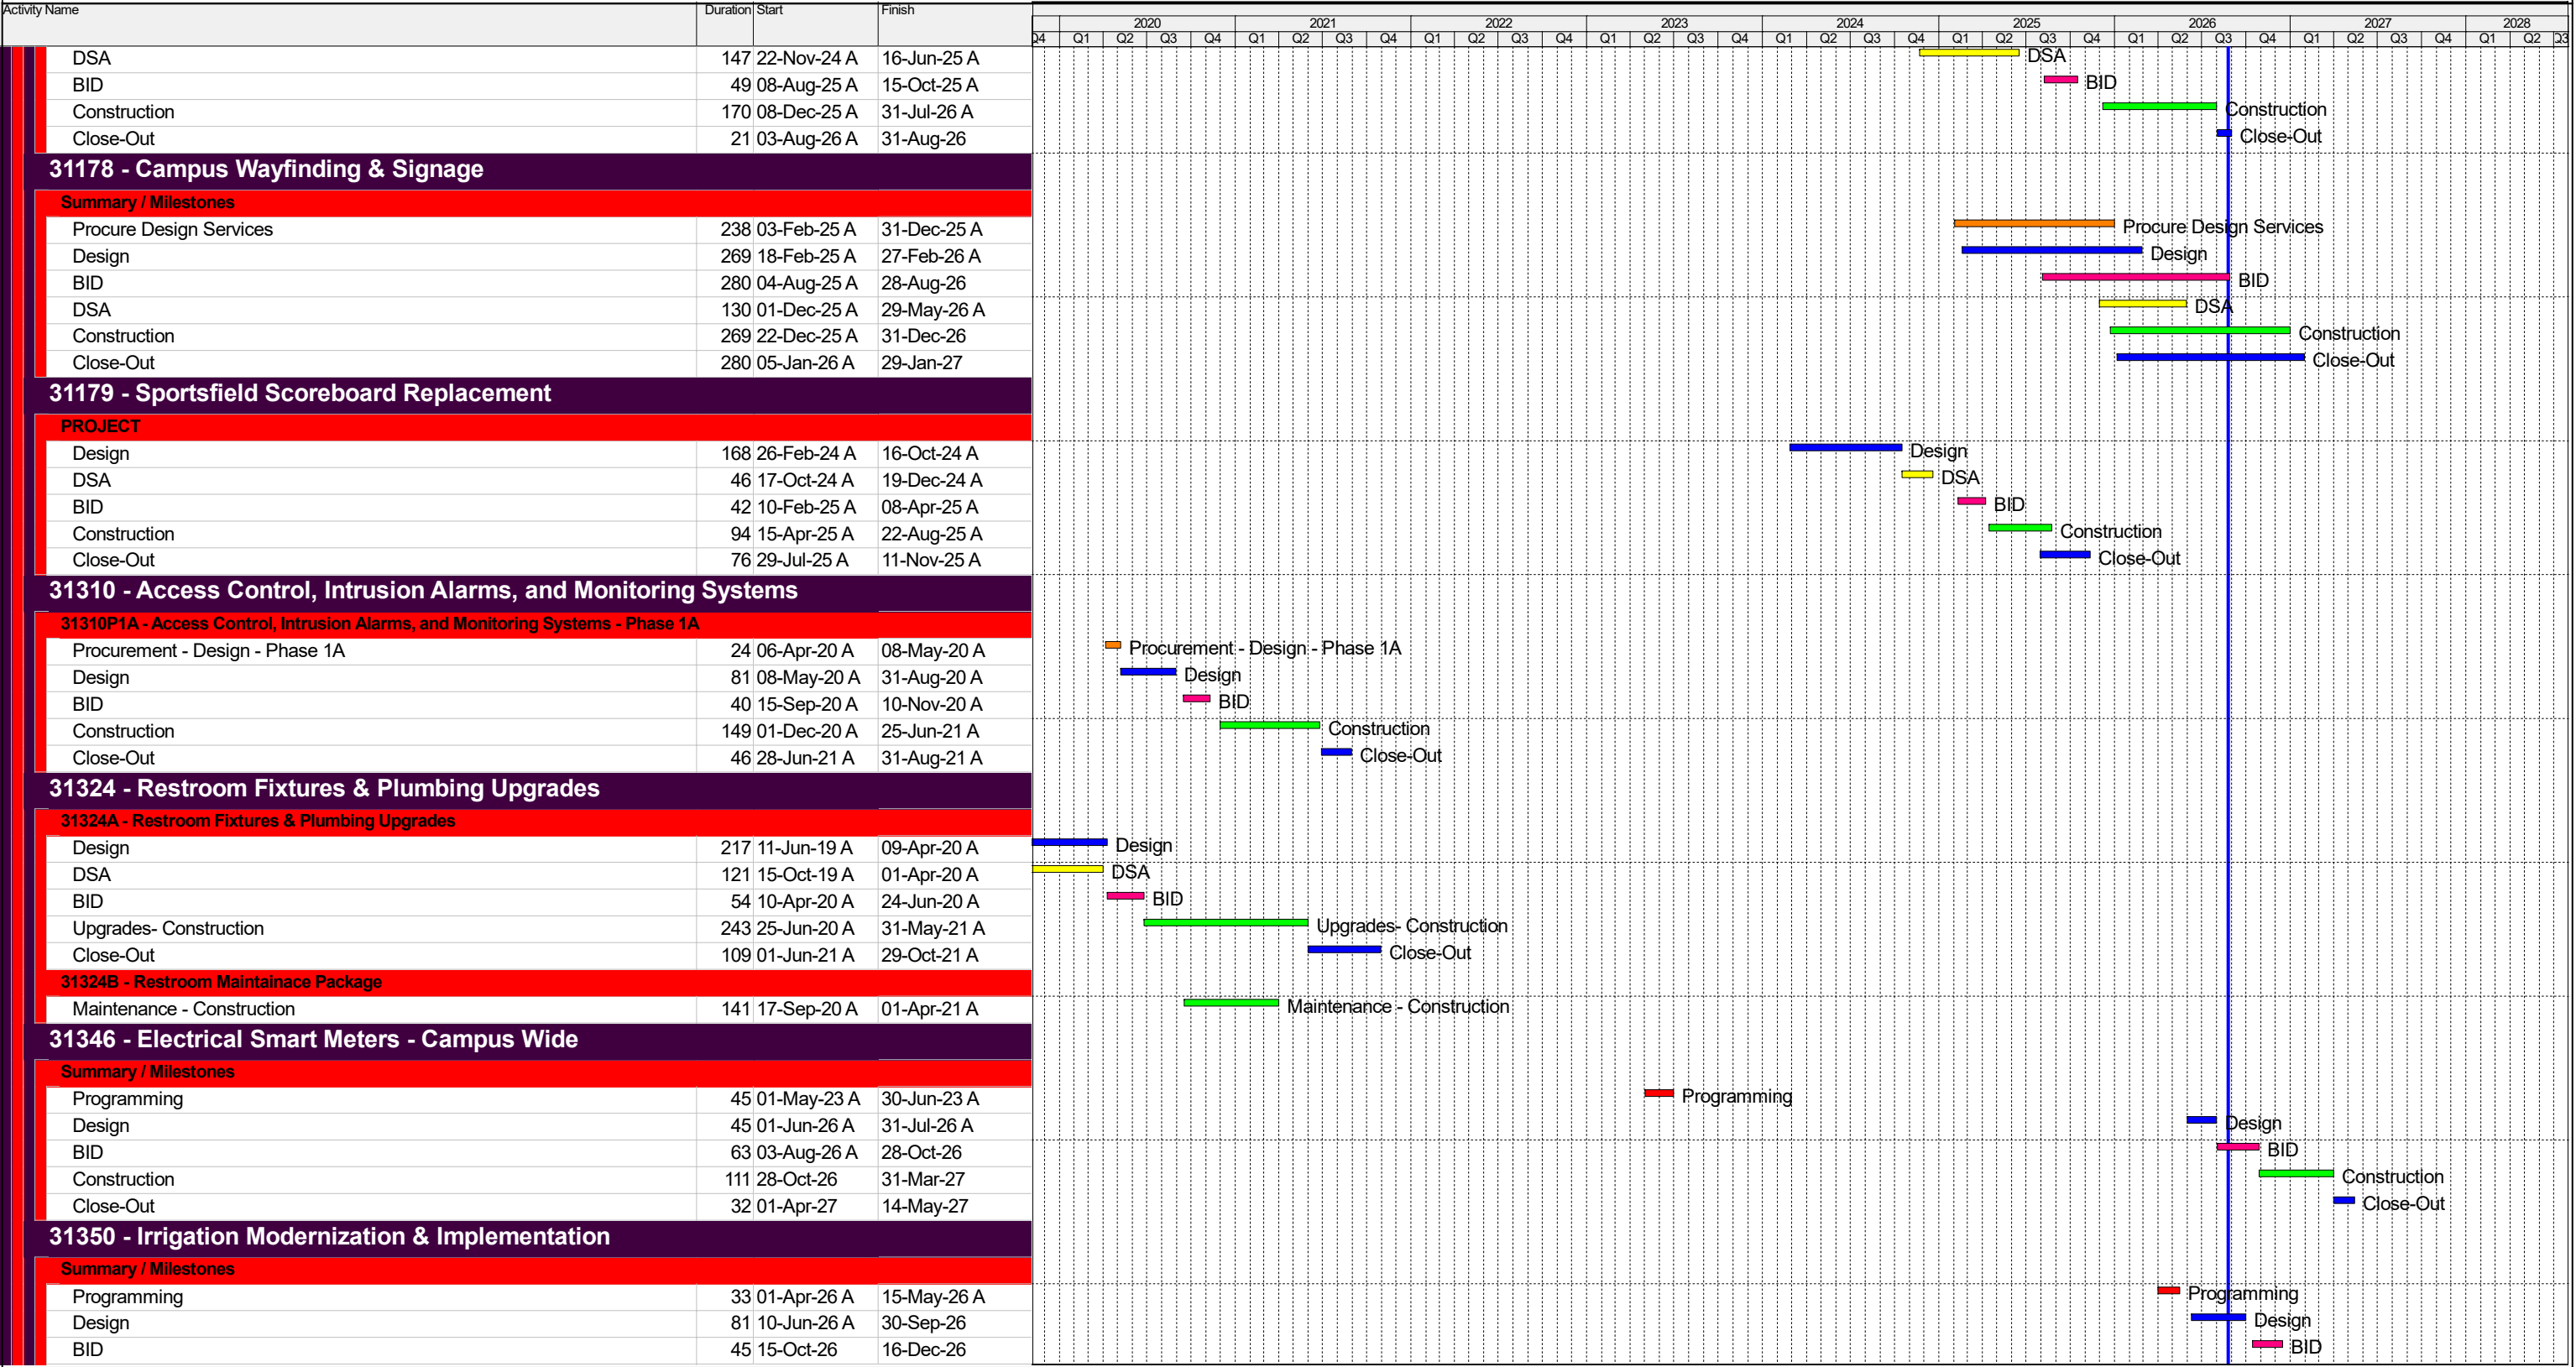

SJECCD Measure X Bond Program Master Schedule

Status as of September 1, 2026

[illegible]

SJECCD Measure X Bond Program Master Schedule
Status as of September 1, 2026

[illegible]

SJECCD Measure X Bond Program Master Schedule
Status as of September 1, 2026

Activity Name				Duration	Start	Finish	Timeline (2020-2028)																															
32138C - Sports Complex CEQA Analysis																																						
Phase 32138C - Programming (Sports Complex CEQA Analysis)				48	17-Jul-20 A	22-Sep-20 A	Phase: 32138C - Programming (Sports Complex CEQA Analysis)																															
32144 - EVC: Campus Painting Project																																						
32144P3A - Phase 3A EVC: Campus Painting Project																																						
BID - Phase 3A				70	20-Dec-19 A	27-Mar-20 A	BID - Phase 3A																															
Construction - Phase 3A				126	17-Mar-20 A	08-Sep-20 A	Construction - Phase 3A																															
Close-Out - Phase 3A				31	09-Sep-20 A	21-Oct-20 A	Close-Out - Phase 3A																															
32144P3B - Phase 3B EVC: Campus Painting Project																																						
BID - Phase 3B				57	06-Mar-20 A	26-May-20 A	BID - Phase 3B																															
Construction - Phase 3B				174	17-Jun-20 A	15-Feb-21 A	Construction - Phase 3B																															
Close-Out - Phase 3B				57	25-Jan-21 A	13-Apr-21 A	Close-Out - Phase 3B																															
32145 - Gullo 2nd Floor - Student Services Center Renovation																																						
Summary / Milestones																																						
Close-Out				185	20-Aug-19 A	04-May-20 A	Close-Out																															
32146 - MS3 Exterior Stair Lighting																																						
Summary / Milestones																																						
Close-Out				212	25-Jun-19 A	15-Apr-20 A	Close-Out																															
32152 - Gullo II Multipurpose Remodel																																						
Summary / Milestones																																						
Design				53	01-Nov-19 A	15-Jan-20 A	Design																															
DSA				97	15-Jan-20 A	29-May-20 A	DSA																															
BID				38	20-Mar-20 A	13-May-20 A	BID																															
Construction				228	14-May-20 A	30-Mar-21 A	Construction																															
Furniture, Fixtures & Equipment- Close-Out				30	19-Oct-20 A	30-Nov-20 A	Furniture, Fixtures & Equipment- Close-Out																															
Move-In (Close-Out)				30	29-Mar-21 A	10-May-21 A	Move-In (Close-Out)																															
Close-Out				30	30-Mar-21 A	10-May-21 A	Close-Out																															
Building Occupancy (Spring 2021)				0		10-May-21 A	Building Occupancy (Spring 2021)																															
32153 - Sequoia Upgrades / Nursing Addition																																						
32153 - Sequoia Upgrades / Nursing Addition																																						
Programming				327	02-Sep-19 A	02-Dec-20 A	Programming																															
Procurement - Design				88	12-Mar-20 A	14-Jul-20 A	Procurement - Design																															
Design				417	30-Nov-20 A	05-Jul-22 A	Design																															
DSA				177	20-Dec-21 A	24-Aug-22 A	DSA																															
BID				191	21-Dec-21 A	13-Sep-22 A	BID																															
32153P1 - Sequoia Nursing Addition																																						
Construction - Nursing Addition				418	14-Oct-22 A	21-May-24 A	Construction - Nursing Addition																															
Furniture, Fixtures & Equipment - Close-Out				186	13-Oct-23 A	28-Jun-24 A	Furniture, Fixtures & Equipment - Close-Out																															
Move-In (Close-Out)				138	23-Jan-24 A	01-Aug-24 A	Move-In (Close-Out)																															
Close-Out				36	22-Mar-24 A	10-May-24 A	Close-Out																															
Building Occupancy (Summer 2024)				0		01-Aug-24 A	Building Occupancy (Summer 2024)																															
32153P2 - Sequoia Nursing Rennovation																																						

Programming

Proc Design

Design

DSA

BID

Construction

Close Out

FFE

Move-In

Milestone

SJECCD Measure X Bond Program Master Schedule
Status as of September 1, 2026

Activity Name			Duration	Start	Finish	Timeline (2020-2028)																															
Construction - Nursing Renovation			136	29-Jul-24 A	03-Feb-25 A	Construction - Nursing Renovation																															
Move-In (Close-Out)			98	30-Oct-24 A	14-Mar-25 A	Move-In (Close-Out)																															
Close-Out			36	17-Jan-25 A	07-Mar-25 A	Close-Out																															
Furniture, Fixtures & Equipment - Close-Out			10	04-Feb-25 A	17-Feb-25 A	Furniture, Fixtures & Equipment - Close-Out																															
Building Occupancy (Winter 2025)			0		14-Mar-25 A	Building Occupancy (Winter 2025),																															
32155 - Cedro Renovation and West Campus ADA Upgrades																																					
Summary / Milestones																																					
Design			160	08-Oct-19 A	19-May-20 A	Design																															
DSA			86	06-Feb-20 A	05-Jun-20 A	DSA																															
BID			54	13-Mar-20 A	28-May-20 A	BID																															
Move-In (Close-Out)			476	21-Aug-20 A	20-Jun-22 A	Move-In (Close-Out)																															
Construction			217	20-Nov-20 A	21-Sep-21 A	Construction																															
Close-Out			419	20-Nov-20 A	29-Jun-22 A	Close-Out																															
Furniture, Fixtures & Equipment - Close-Out			412	20-Nov-20 A	20-Jun-22 A	Furniture, Fixtures & Equipment - Close-Out																															
Building Occupancy (Summer 2022)			0		20-Jun-22 A	Building Occupancy (Summer 2022),																															
32156 - General Education Building																																					
Summary / Milestones																																					
Procurement - Design			88	26-May-20 A	25-Sep-20 A	Procurement - Design																															
Programming			47	08-Sep-20 A	11-Nov-20 A	Programming																															
Design			348	09-Sep-20 A	10-Jan-22 A	Design																															
DSA			247	14-Dec-21 A	23-Nov-22 A	DSA																															
BID			52	02-May-22 A	12-Jul-22 A	BID																															
Construction			487	11-Aug-22 A	21-Jun-24 A	Construction																															
Move-In (Close-Out)			253	22-Jun-23 A	10-Jun-24 A	Move-In (Close-Out)																															
Building Occupancy (Summer 2024)			0		10-Jun-24 A	Building Occupancy (Summer 2024),																															
Close-Out			117	22-Jul-24 A	31-Dec-24 A	Close-Out																															
Furniture, Fixtures & Equipment - Close-Out			36	09-Aug-24 A	30-Sep-24 A	Furniture, Fixtures & Equipment - Close-Out																															
32157 - Student Activities Center - ON HOLD -																																					
Summary / Milestones																																					
Programming			522	03-Jun-19 A	01-Jun-21 A	Programming																															
Procurement - Design			76	01-Sep-21 A	15-Dec-21 A	Procurement - Design																															
Design			359	15-Dec-21 A	01-May-23 A	Design																															
DSA			129	03-May-23 A	30-Oct-23 A	DSA																															
BID			65	31-Oct-23 A	29-Jan-24 A	BID																															
Construction			391	31-Jan-24 A	30-Jul-25 A	Construction																															
Close-Out			65	31-Jul-25 A	29-Oct-25 A	Close-Out																															
Furniture, Fixtures & Equipment - Close-Out			63	31-Jul-25 A	27-Oct-25 A	Furniture, Fixtures & Equipment - Close-Out																															
Move-In (Close-Out)			63	31-Jul-25 A	27-Oct-25 A	Move-In (Close-Out)																															
Building Occupancy (Fall 2025)			0		27-Oct-25 A	Building Occupancy (Fall 2025),																															
32158 - West Campus ADA Upgrades																																					
Summary / Milestones																																					
Design			160	08-Oct-19 A	18-May-20 A	Design																															
BID			158	17-Mar-20 A	22-Oct-20 A	BID																															
DSA			73	19-May-20 A	27-Aug-20 A	DSA																															
Construction			237	23-Oct-20 A	21-Sep-21 A	Construction																															
Close-Out			207	15-Jul-21 A	29-Apr-22 A	Close-Out																															
Close-Out Complete			0		29-Apr-22 A	Close-Out Complete,																															




SJECCD Measure X Bond Program Master Schedule Status as of September 1, 2026


Activity Name	Duration	Start	Finish	Timeline (2020-2028)																											
32159 - Campus Way Finding / Ground Lighting																															
Summary / Milestones																															
Design	199	03-Jun-19 A	06-Mar-20 A																												
DSA	243	06-Feb-20 A	11-Jan-21 A																												
BID	65	25-Feb-20 A	26-May-20 A																												
Construction	554	17-Mar-20 A	02-May-22 A																												
Close-Out	364	02-Mar-22 A	24-Jul-23 A																												
32160 - Security Hardware																															
Summary / Milestones																															
BID	59	21-Nov-19 A	12-Feb-20 A																												
Construction	95	12-Feb-20 A	24-Jun-20 A																												
Close-Out	66	31-Mar-20 A	01-Jul-20 A																												
32161 - North Fire Lane / ADA																															
Summary / Milestones																															
Design	294	01-Nov-19 A	17-Dec-20 A																												
DSA	98	17-Jul-20 A	01-Dec-20 A																												
BID	132	31-Jul-20 A	01-Feb-21 A																												
Construction	560	09-Feb-21 A	03-Apr-23 A																												
Furniture, Fixtures & Equipment / Make Ready for Occupancy	250	15-Feb-21 A	31-Jan-22 A																												
Close-Out	86	17-Jan-23 A	16-May-23 A																												
32163 - Campus-Wide Building Signage																															
PROJECT																															
Procurement - Design	51	03-Feb-20 A	14-Apr-20 A																												
Design	93	15-Apr-20 A	21-Aug-20 A																												
BID	82	24-Aug-20 A	16-Dec-20 A																												
Construction	148	17-Dec-20 A	13-Jul-21 A																												
Close-Out	22	01-Sep-21 A	30-Sep-21 A																												
32164 - EVC CEQA Compliance Consulting Service																															
Summary / Milestones																															
Procurement - Design	78	21-Feb-20 A	10-Jun-20 A																												
Design	422	27-Mar-20 A	09-Nov-21 A																												
Administrative Draft EIR	55	19-Apr-21 A	05-Jul-21 A																												
Administrative Final EIR	16	27-Sep-21 A	19-Oct-21 A																												
32165 - MS3 Canopy																															
32165 - MS3 Canopy																															
Design	169	13-Mar-20 A	05-Nov-20 A																												
DSA	140	28-Jul-20 A	08-Feb-21 A																												
BID	111	09-Feb-21 A	14-Jul-21 A																												
Construction	173	14-Jul-21 A	15-Mar-22 A																												
Close-Out	32	03-Oct-22 A	15-Nov-22 A																												
32166 - SSC Entry Road and Parking Lot																															
Summary / Milestones																															
Design (Phase I - Entry Road and Parking Lot)	596	20-Jan-20 A	02-May-22 A																												
DSA	100	24-Mar-21 A	11-Aug-21 A																												
BID	158	07-Apr-21 A	13-Nov-21 A																												
Construction	543	01-Dec-21 A	29-Dec-23 A																												



SJECCD Measure X Bond Program Master Schedule
Status as of September 1, 2026

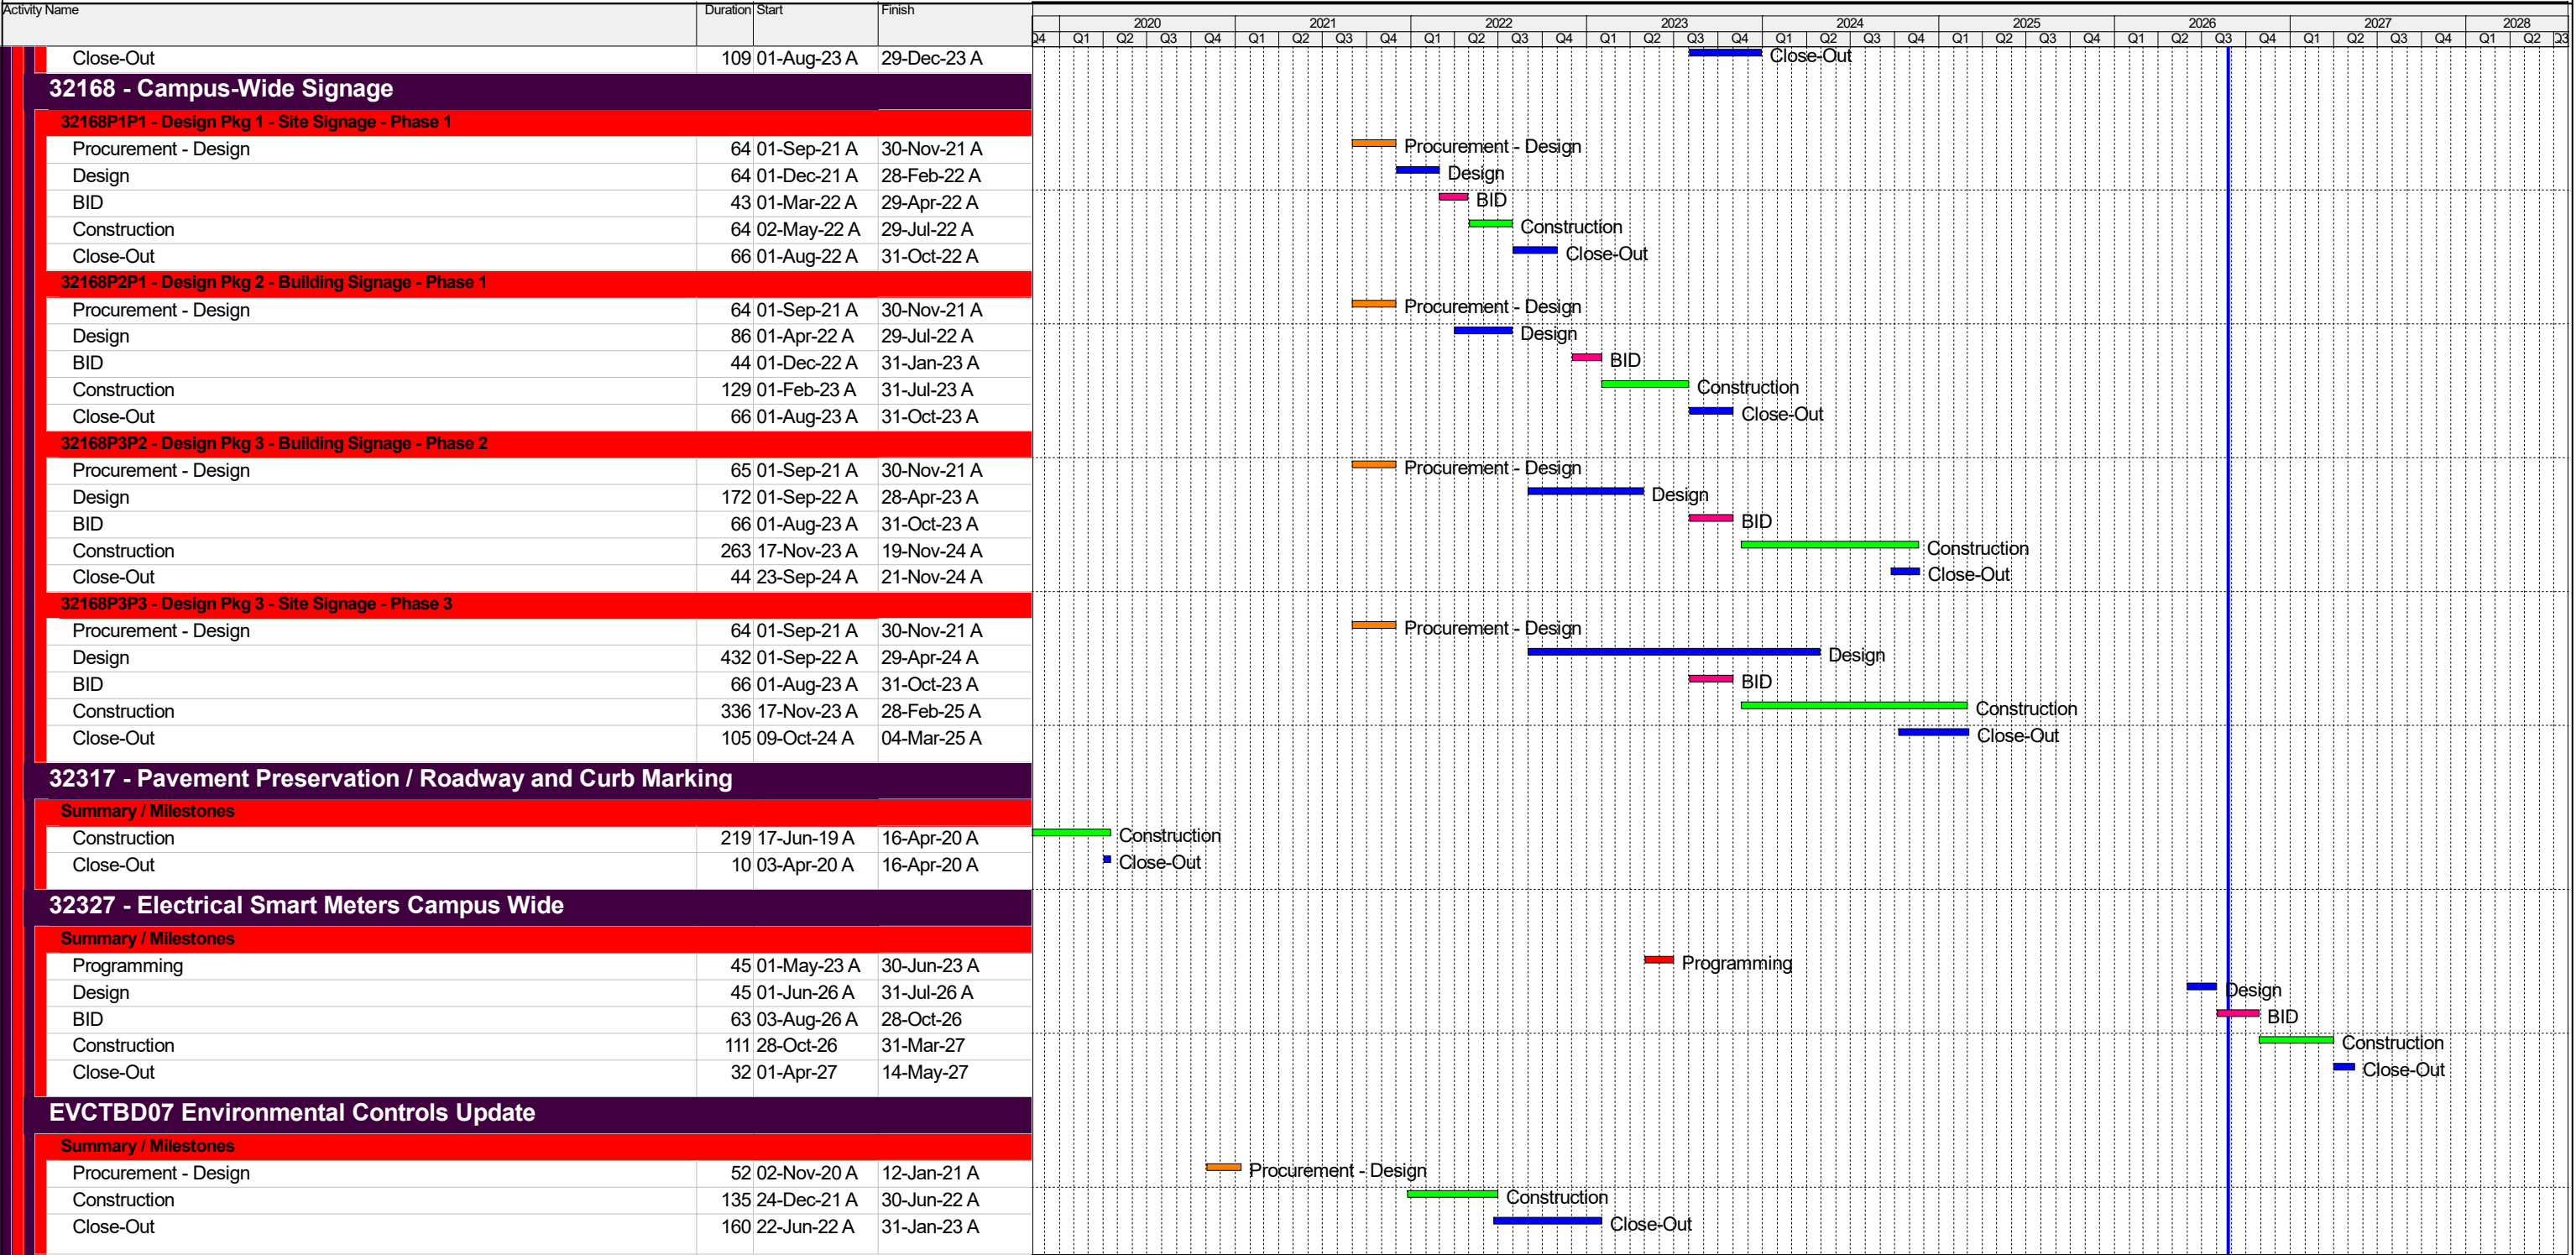

SJECCD Measure X Bond Program Master Schedule
Status as of September 1, 2026

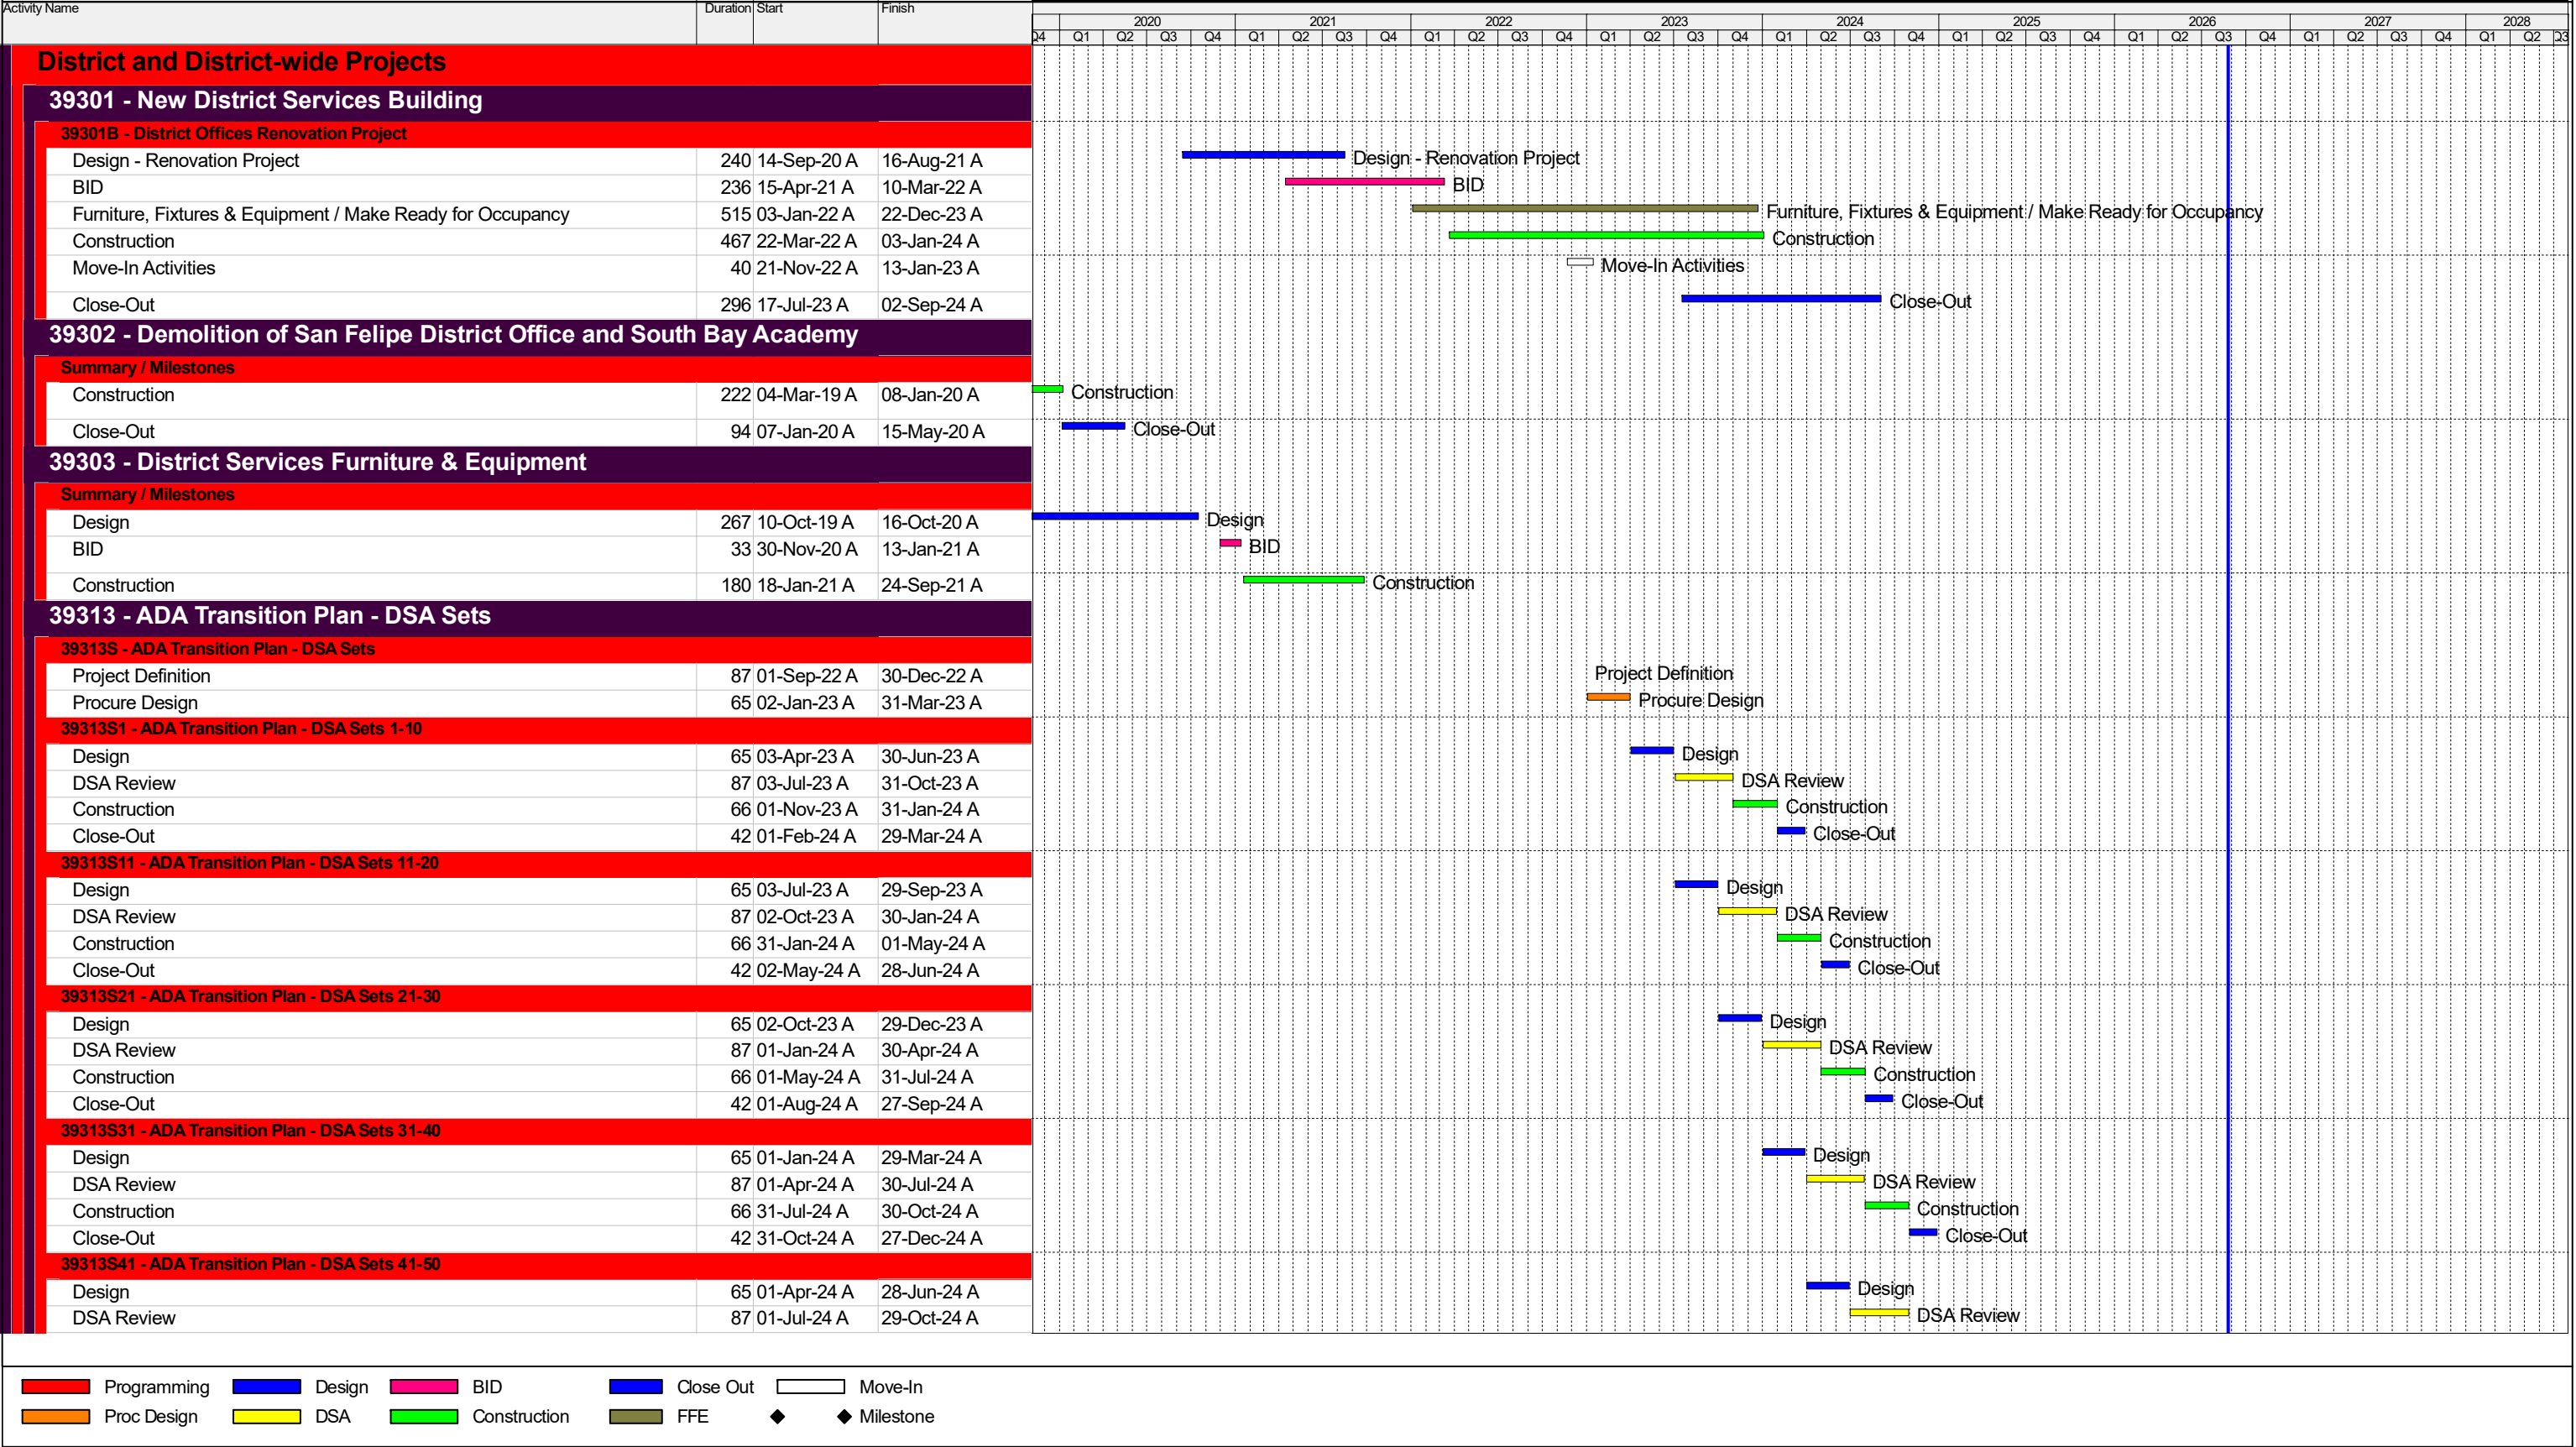

SJECCD Measure X Bond Program Master Schedule Status as of September 1, 2026

Activity Name			Duration	Start	Finish
Construction			66	30-Oct-24 A	29-Jan-25 A
Close-Out			42	30-Jan-25 A	28-Mar-25 A
39314 - District Office Elevators Safety and Accessibility Upgrades					
Summary / Milestones					
Design			59	02-Dec-19 A	21-Feb-20 A
BID			83	17-Feb-20 A	10-Jun-20 A
Construction			283	02-Jun-20 A	01-Jul-21 A
Close-Out			31	02-Jul-21 A	13-Aug-21 A
39315 - District Elevator Assessment					
Summary / Milestones					
Procurement - Design			55	26-Nov-19 A	11-Feb-20 A
Design			128	12-Feb-20 A	07-Aug-20 A
39629 - District Warehouse & Operations Facility					
39629P1 - District Wearhouse & Operations Facility - Phase 1					
Project Definition			64	02-May-22 A	29-Jul-22 A
Procure Design			132	01-Aug-22 A	31-Jan-23 A
Programming			63	01-Feb-23 A	28-Apr-23 A
Design			219	01-May-23 A	29-Feb-24 A
DSA Review			86	01-Mar-24 A	28-Jun-24 A
Construction - New Addition & Site			196	01-Jul-24 A	31-Mar-25 A
Close-Out			65	01-Apr-25 A	30-Jun-25 A
39629P2 - District Wearhouse & Operations Facility - Phase 2					
Construction - Renovation			195	02-Jun-25 A	27-Feb-26 A
Close-Out			65	02-Mar-26 A	29-May-26 A
39632 - District Wide Central Plant Upgrade					
Summary / Milestones					
Procurement - Design			85	01-Apr-22 A	29-Jul-22 A
Design			152	01-Aug-22 A	28-Feb-23 A
DSA			260	02-Dec-24 A	28-Nov-25 A
Construction			262	13-Jan-26 A	13-Jan-27
Close-Out			65	15-Jan-27	15-Apr-27

